



# WWTP-201 WASTEWATER SYSTEM # 120002264

## ANNUAL WASTEWATER REPORT

**PREPARED FOR**  
The Township of Ramara

**SUBMITTED BY**  
Ontario Clean Water Agency  
2115 Highway 12, Brechin, ON L0K 1B0

Reporting period of January 1, 2025 to December 31, 2025

Issued: April 22, 2026

Revision: 1

Operating Authority: Ontario Clean Water Agency (OCWA)

## Table of Contents

1. Background .....	1, 2
2. Summary of Influent Flow Data .....	3, 4
3. Hydraulic Reserve Capacity.....	4
4. Summary of Effluent Flow Data .....	4, 5
5. Summary of Sampling Frequency .....	5, 6
6. Final Effluent Parameter Summary 6 - .....	9
7. Description of Operating Problems .....	10
8. Summary of Maintenance .....	10, 11
9. Summary of Effluent Quality Assurance and Control Measures.....	11, 12
10. Summary of Calibration and Maintenance .....	12
11. Description of Efforts Made and Results Achieved to Meet Effluent Objectives 12 - .....	17
12. Summary of Biosolids .....	17
13. Summary of Community Complaints.....	17
14. Summary of By-passes, Spills and Other Discharges.....	17
15. Status Update on Initial Effluent Characterization.....	17
16. Additional Information the District Manger Requested .....	17
17. Summary of Efforts Made to Reduce Overflows, Spills and Bypasses .....	17, 18

## Appendices

Appendix I Performance Assessment Report

Appendix II Annual Calibration Reports

Appendix III Biosolids Summary

Appendix IV Weekly Effluent Parameter Reports

## List of Tables

Table 1	Historical Sewage Flows and Generation Rates
Table 2	Minimum Raw Sewage Sampling Requirements
Table 3	Minimum Effluent Sampling Requirements
Table 4	Annual Average Concentration and Loading 2025
Table 5	Brechin Lagoon City WWTP Operational Challenges 2025
Table 6	Brechin Lagoon City WWTP – Summary of Equipment Calibrations 2025
Table 7	Efforts Made to Meet the Effluent Objectives of Condition 9
Table 8	Final Effluent Monthly CBOD5 Concentration Objective Comparisons 2025
Table 9	Final Effluent Monthly TSS Concentration Objective Comparisons 2025
Table 10	Final Effluent Monthly Total Phosphorus Concentration Objective Comparisons 2025
Table 11	Final Effluent Monthly E. Coli GMD Objective Comparisons 2025
Table 12	Final Effluent Monthly pH Concentration Objective Comparisons 2025
Table 13	Weekly Final Effluent pH, Temperature and Calculated Un-ionized Ammonia 2025
Table 14	Monthly Influent Average Concentrations 2025
Table 15	Monthly Sludge Generation Volumes 2025
Table 16	Summary of Complaints 2025
Table 17	Summary of Events 2025

## 1. Background

The Environmental Compliance Approval (ECA) No. 1114-745MQT issued on June 6<sup>th</sup>, 2007 was revoked and replaced by ECA No. 8497-8D3TU7 issued on June 28<sup>th</sup>, 2012. The Ontario Clean Water Agency was the operating authority during the reporting period January 1<sup>st</sup> - December 31<sup>st</sup>, 2025.

The Brechin/Lagoon City Sewage Works complies with all requirements of the regulating authorities and operates under:

- Environmental Compliance Approval (ECA) No. 8497-8D3TU7 issued June 28, 2012
- Environmental Compliance Approval (CLI-ECA) No. 147-W601 Issue 2 issued July 22, 2024

*Environmental Certificate of Approval (ECA) No. 8497-8D3TU7 Section 9(5) requires the Performance Report to contain the following:*

- a) *Summary and interpretation of all monitoring data and a comparison to the effluent limits outlined in Condition 5, including an overview of the success and adequacy of the sewage Works;*
- b) *a description of any operating problems encountered and corrective actions taken;*
- c) *a summary of all maintenance carried out on any major structure, equipment, apparatus, mechanism or thing forming part of the Works;*
- d) *a summary of any effluent quality assurance or control measures undertaken in the reporting period;*
- e) *a summary of the calibration and maintenance carried out on all effluent monitoring equipment;*
- f) *a description of efforts made and results achieved in meeting the Design Objectives of Condition 4;*
- g) *a tabulation of the volume of sludge generated in the reporting period, an outline of anticipated volumes to be generated in the next reporting period and a summary of the locations to where the sludge was disposed;*
- h) *a summary of any complaints received during the reporting period and any steps taken to address the complaints;*
- i) *a summary of all By-pass, spill or abnormal discharge events;*
- j) *Status update of the initial effluent characterization as per Condition 8 subsection (1) until it has been completed and the required report has been submitted; and*
- k) *any other information the District Manager requires from time to time*

*Environmental Compliance Approval (CLI-ECA) No. 147-W601 Issue 2 issued July 22, 2024 Section 4.6 requires the Performance Report to contain the following:*

- a) *A summary of all required monitoring data along with an interpretation of the data and any conclusion drawn from the data evaluation about the need for future modifications to the Authorized System or system operations.*
- b) *A summary of any operating problems encountered and corrective actions taken.*
- c) *A summary of all calibration, maintenance and repairs carried out on any major structure, Equipment, apparatus, mechanism, or thing forming part of the Municipal Sewage Collection System.*
- d) *A summary of complaints related to the Sewage Works received during the reporting period and any steps taken to address the complaints.*
- e) *A summary of Alterations to the Authorized System within the reporting period that are authorized by this Approval including a list of Alterations that pose a Significant Drinking Water Threat.*
- f) *A summary of all Collection System Overflow(s) and Spill(s) of Sewage, including:*
  - i) *Dates;*
  - ii) *Volumes and durations;*
  - iii) *If applicable, loading for total suspended solids, BOD, total phosphorus, and total Kjeldahl nitrogen, and sampling results for E. coli;*
  - iv) *Disinfection, if any; and*
  - v) *Any adverse impact(s) and corrective actions, if applicable.*
- g) *A summary of efforts made to reduce Collection System Overflows, Spills, STP Overflows, and/or STP Bypasses, including items, as applicable:*
  - i) *A description of projects undertaken and completed in the Authorized System that result in overall overflow reduction or elimination including expenditures and proposed projects to eliminate overflows with estimated budget forecast for the year following that for which the report is submitted.*
  - ii) *Details of the establishment and maintenance of a PPCP, including a summary of project progresses compared to the PPCP's timelines.*
  - iii) *An assessment of the effectiveness of each action taken.*
  - iv) *An assessment of the ability to meet Procedure F-5-1 or Procedure F-5-5 objectives (as applicable) and if able to meet the objectives, an overview of next steps and estimated timelines to meet the objectives.*
  - v) *Public reporting approach including proactive efforts.*

This report will show that the Ontario Clean Water Agency has made every attempt to achieve its goals through its operational performance. This performance was enhanced through the use of an electronic process data collection database, an electronic maintenance and work order database, an electronic operational excellence database, a training program focused on providing the right skills to staff - also captured and tracked by the use of an electronic database and a multi-skilled, flexible workforce.

This report will show that the requirements of the facility ECA including effluent monitoring and reporting requirements were consistently met and that effluent quality under normal conditions was consistently within ECA requirements, with the exception for the month of March where exceedances were reported as a result of operating outside normal conditions.


## 2. Summary of Influent Flow Data

Environmental Compliance Approval (ECA) No. 8497-8D3TU7, issued for the Brechin/Lagoon City WWTP Condition 9(5)(a) requires a Summary and interpretation of all monitoring data and a comparison to the effluent limits outlined in Condition 5, including an overview of the success and adequacy of the sewage Works.


Condition 4(2)(b) of the (ECA) No. 8497-8D3TU7 indicates best efforts are to be made to operate at the rated capacity of the works. The rated capacity for the Brechin/Lagoon City Wastewater Treatment Plant is 2,273 m<sup>3</sup>/day and the annual average daily influent flow was 1,432.68 m<sup>3</sup>/day or 63.03 % of the rated capacity.

The total Influent flow in 2025 was 522,929.93 m<sup>3</sup>

Graph 1: Influent Flow Monthly Totals for 2025

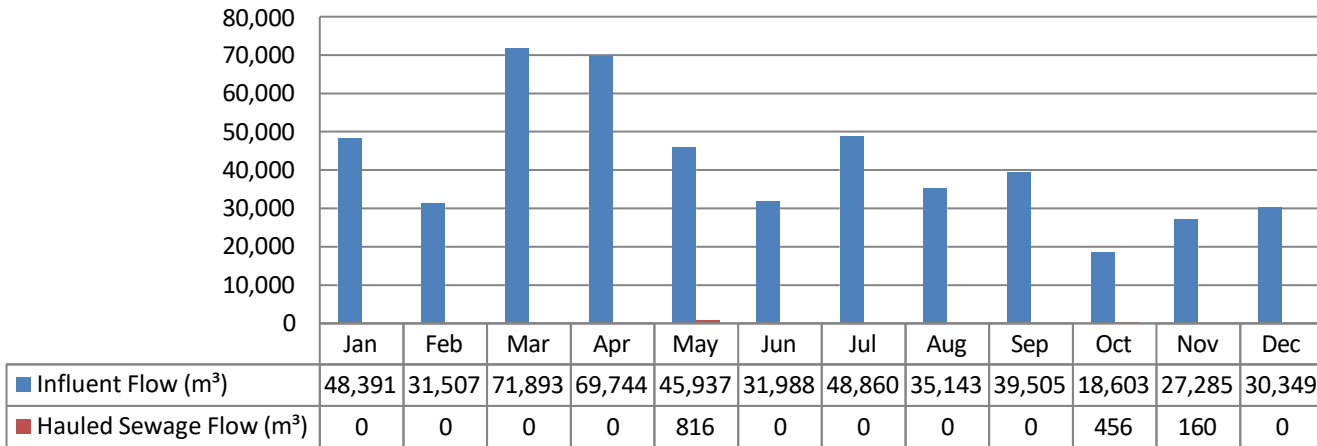

Graph 2: Influent Daily Minimum, Maximum and Average Flows for 2025

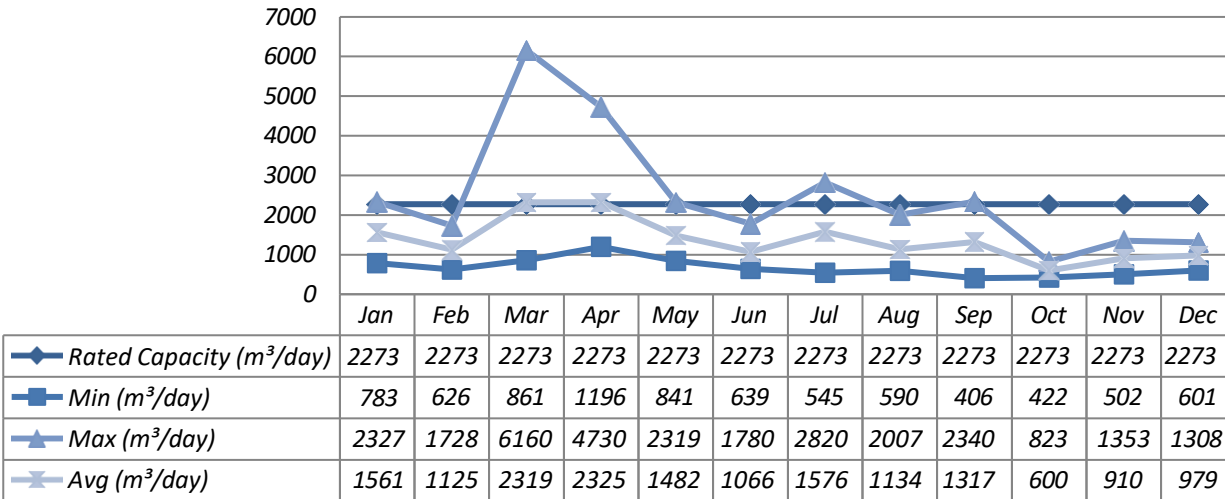

Note: The above table shows exceedances in maximum flows. The spikes in flows were due to weather events/snowmelt in correlation with significant inflow and infiltration during these weather events. The average daily flow for the works was below the rated capacity, excluding March and April, which was reported and monitored as a bypass.

Brechin Lagoon City Sewage Works Historical Flows

TABLE 1: HISTORICAL SEWAGE FLOWS AND GENERATION RATES						
Year	Number of Connections*	Equivalent Population**	Average Daily Flow (m <sup>3</sup> /day)	Maximum Daily Flow (m <sup>3</sup> /day)	Rated Capacity (m <sup>3</sup> /day)	Sewage Generation Rate (L/cap/day)
2015	1162	2414	1262	3313	2273	523
2016	1165	2420	1255	4735	2273	517
2017	1170	2431	1566	4213	2273	644
2018	1174	2439	1430	4260	2273	586
2019	1175	2441	1481	3686	2273	607
2020	1179	2650	1393	3462	2273	526
2021	1179	2650	1257	3995	2273	474
2022	1140	2391	1165	3853	2273	487
2023	1142	2395	1351	4687	2273	564
2024	1142	2395	1538	3793	2273	642
2025	1197	2395	1368	6160	2273	571
3 Year Average		2395	1419	4880	2273	592

\*In 2025 the number of connections were recalculated based on property-level verification completed by the Township of Ramara.

\*\*Based on estimated service connections in Lagoon City and Brechin: 1045 and 152 single family dwellings. The estimated population in Lagoon City: 2,000 (based on a population density of 2.0 persons per dwelling), and the estimated population in Brechin: 395 (based on a population density of 2.6 persons per dwelling). Assumptions made on location of new developments for 2025 connections for population estimation.

Note: This calculation was completed based on current connections in the system, growth within the collection system has not been considered.

3. Hydraulic Reserve Capacity

In accordance with the MECP Procedure D-5-1, the reserve capacity is calculated by the following formula:  
 Hydraulic Reserve Capacity= Design Flow- Committed Flow

The design flow is equal to the maximum permissible flow approved by the Amended Environmental Compliance Approval. (ECA) No. 8497-8D3TU7 maximum permissible flow is: 2273 m<sup>3</sup>/day. The committed flow is equal to the total expected flow by the existing and proposed connections based on the previous 3-year average daily flow.

The built-out service area of the Brechin/Lagoon City Sewage Works has a total of 1197 units. The three-year (2023-2025) average sewage generation rate is: 592 L/cap/day. With the current population of 2395 there is a projection of 1,418 m<sup>3</sup>/day of committed sewage flow. The estimated hydraulic reserve capacity for the Brechin Lagoon City Sewage Works in 2025 is 855 m<sup>3</sup>/day.

\*These aspects of the report are generated from available data and are intended for operational reporting and not for future capacity assumptions. To help ensure a wastewater treatment plant is adequately sized to

accommodate additional service connections without compromising its efficiency or environmental impact, a thorough review should be undertaken which should include but not be limited to sewer capacity, design flow, retention time, future population growth, industrial wastewater, infiltration and inflow, and other relevant factors.


4. Summary of Effluent Flow Data

Environmental Compliance Approval (ECA) No. 8497-8D3TU7, issued for the Brechin/Lagoon City WWTP Condition 9(5)(a) requires a summary and interpretation of all monitoring data and a comparison to the effluent limits outlined in Condition 5, including an overview of the success and adequacy of the sewage works.


Condition 4(2)(b) of the (ECA) No. 8497-8D3TU7 indicates best efforts are to be made to operate at the rated capacity of the works. The rated capacity for the Brechin/Lagoon City Wastewater Treatment Plant is 2,273 m<sup>3</sup>/day and the annual average daily effluent flow was 1,455.07m<sup>3</sup>/day or 64.0 % of the rated capacity

The total effluent flow in 2025 was 531 102 m<sup>3</sup>

Graph 3: Effluent Flow Monthly Totals for 2025

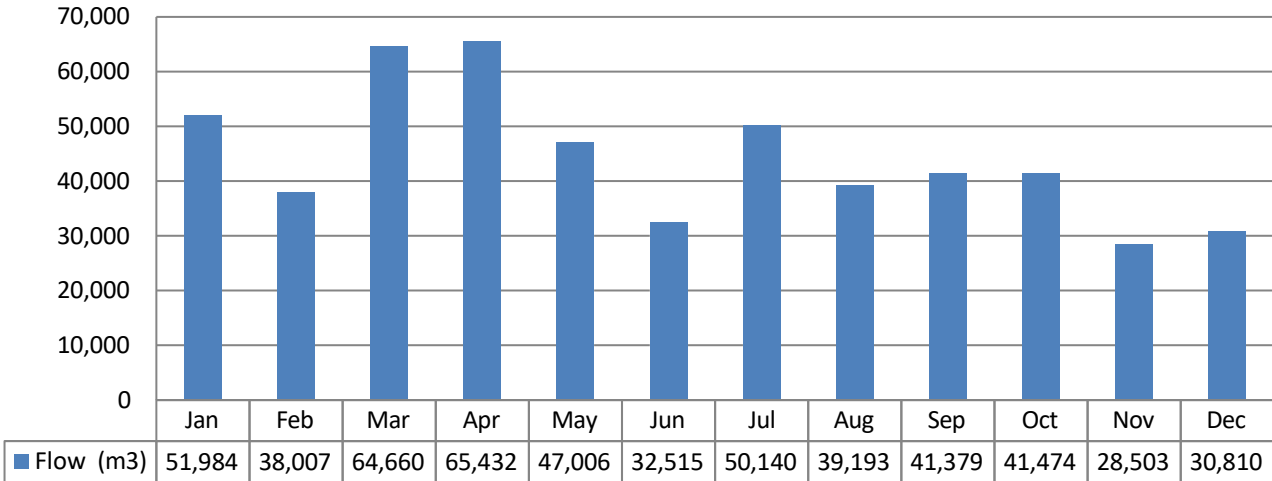

Graph 4: Effluent Daily Minimum, Maximum and Average Flows for 2025

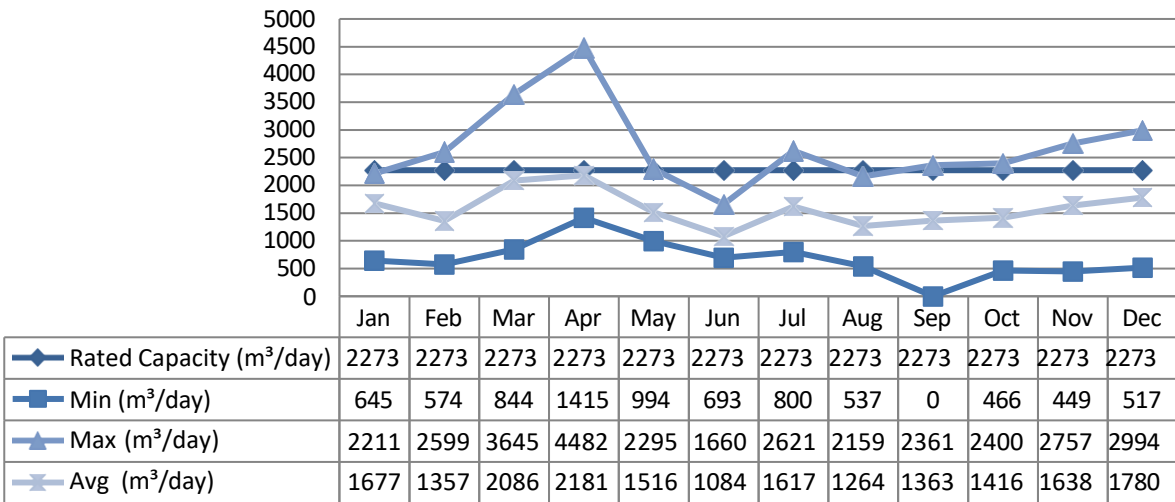

Note: The above table shows exceedances in maximum flows. The spikes in flows were due to weather events/snowmelt in correlation with significant inflow and infiltration during these weather events. However, the average daily flow for the works was below the rated capacity. The min value for September is a result of a scheduled plant shut down for maintenance.

## 5. Summary of Sampling Frequency

ECA No. 8497-8D3TU7 Condition 7(3) describes the requirement for sample collection at the following locations, frequencies and by means of the specified sample type and analyzed for each parameter listed and all results recorded:

TABLE 2: MINIMUM RAW SEWAGE SAMPLING REQUIREMENTS		
Influent Sampling Point		
Parameters	Sample Type	Frequency
BOD5	8 Hour Daytime Composite	Monthly
Total Suspended Solids	8 Hour Daytime Composite	Monthly
Total Phosphorus	8 Hour Daytime Composite	Monthly
Total Kjeldahl Nitrogen	8 Hour Daytime Composite	Monthly

TABLE 3: MINIMUM EFFLUENT SAMPLING REQUIREMENTS		
Final Effluent Sampling Point		
Parameters	Sample Type	Frequency
CBOD5	24-Hour Composite	Weekly
Total Suspended Solids	24-Hour Composite	Weekly
Total Phosphorus	24-Hour Composite	Weekly
Total Ammonia Nitrogen	24-Hour Composite	Weekly
Nitrates	24-Hour Composite	Weekly
pH	Grab/Probe	Weekly
Temperature	Grab/Probe	Weekly
E. coli	Grab	Weekly

## 6. Final Effluent Parameter Summary


The following tables provide a summary of the monitoring data for the Brechin/Lagoon City WWTP compared to the effluent limits and objectives outlined in Condition 4 and 5 of ECA No. 8497-8D3TU7.

A summary of the Final Effluent and Raw Sewage monitoring data is contained in Appendix I of this report.

### Carbonaceous Biochemical Oxygen Demand (CBOD5)

ECA No. 8497-8D3TU7 sets the final effluent monthly CBOD5 average concentration limit at 10.00 mg/L and the objective limit at 8.0 mg/L. The final effluent monthly CBOD5 average concentration results throughout 2025 were in compliance with the concentration limit and the objective limit as outlined in ECA No. 8497-8D3TU7.


Graph 5: Final Effluent Monthly CBOD5 Concentration Comparisons for 2025

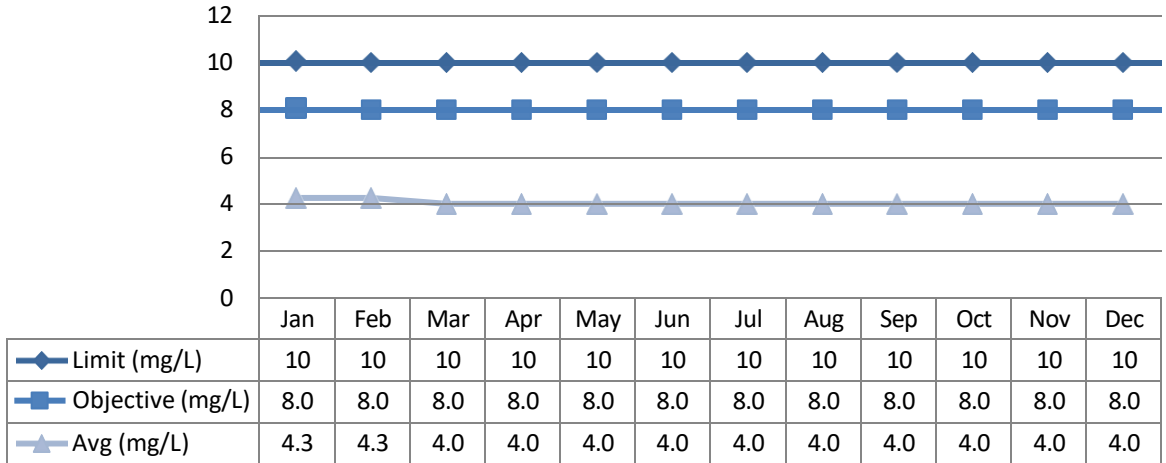

**Total Suspended Solids (TSS)**

ECA No. 8497-8D3TU7 sets the final effluent monthly TSS average concentration limit at 15.0 mg/L and the objective limit at 12.0 mg/L. The final effluent monthly TSS average concentration results throughout 2025, with the exception of the month of March, were in compliance with the limits and objectives outlined in ECA No. 8497-8D3TU7.

Graph 6: Final Effluent Monthly TSS Concentration Comparisons for 2025

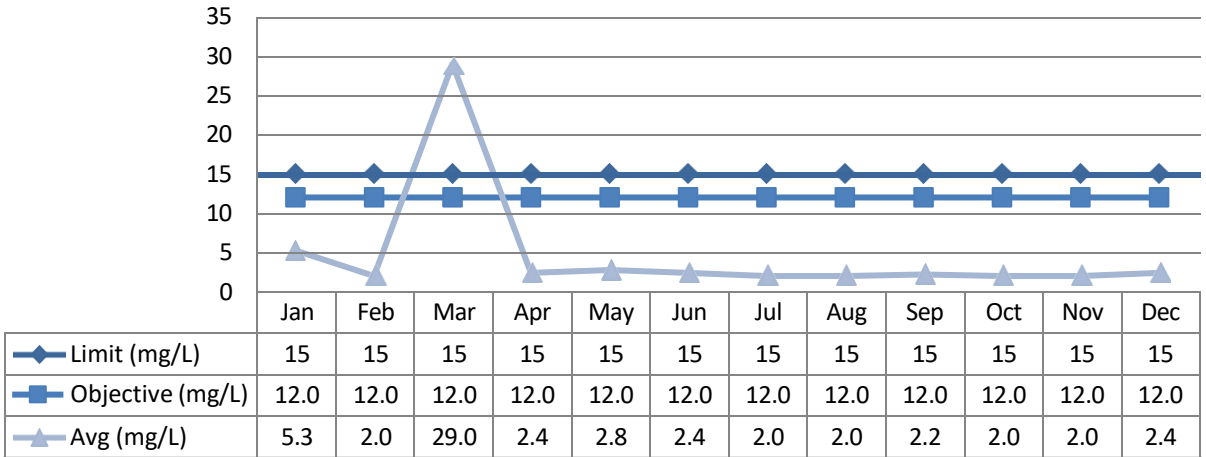


*Note: The above table shows an exceedance in the month of March which occurred as a result of a bypass and was reported to the Ministry of the Environment Conservation and Parks District Manager.*

**Total Phosphorus (TP)**

ECA No. 8497-8D3TU7 sets the final effluent TP monthly concentration limit at 0.30 mg/L, the objective limit at 0.24mg/L and the annual average waste loading at 249 kg/year. The final effluent monthly TP average concentration results, with the exception of the month of March, and annual average waste loading results throughout 2025 were in compliance with the limits and objectives outlined in ECA No. 8497-8D3TU7.

Condition 5(2) of ECA No. 8497-8D3TU7 lists the Lake Simcoe Phosphorus Reduction Strategy effluent limits. These limits are set at an annual average concentration of 0.15 mg/L and annual average loading of 124 kg/Year.

Graph 7: Final Effluent Monthly Total Phosphorus Concentration Comparisons for 2025

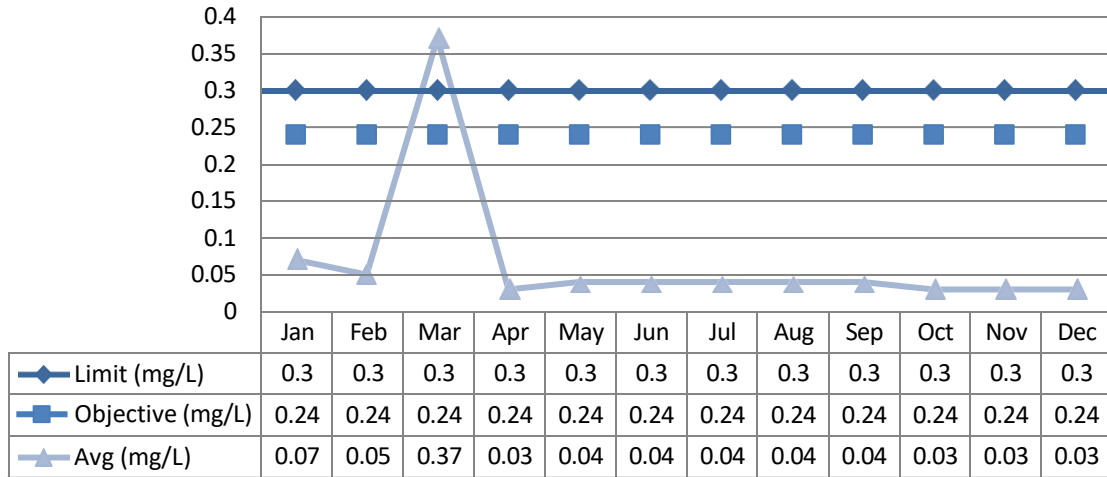

Note: The above table shows an exceedance in March which occurred as a result of a bypass and was reported to the Ministry of the Environment Conservation and Parks District Manager.


TABLE 4: ANNUAL AVERAGE CONCENTRATION AND LOADING 2025

Parameters	2025 Annual Average Concentration (mg/L)	Lake Simcoe Annual Average Concentration Limit /Objective	2025 Annual Average Loading (Kg/year)	Annual Loading Limit (Kg/year)	Lake Simcoe Annual Concentration Limit/Objective (mg/L)	Compliant (Y/N)
Total Phosphorus	0.09	0.15	49.67	249	124	Yes

E. Coli

ECA No. 8497-8D3TU7 sets the final effluent monthly geometric mean density of E. Coli at 200 cfu/100mL and an objective limit of 100 cfu/100ml. The final effluent monthly geomean limits were met each month in 2025.


Graph 9: Final Effluent Monthly E. Coli Geometric Mean Comparisons for 2025

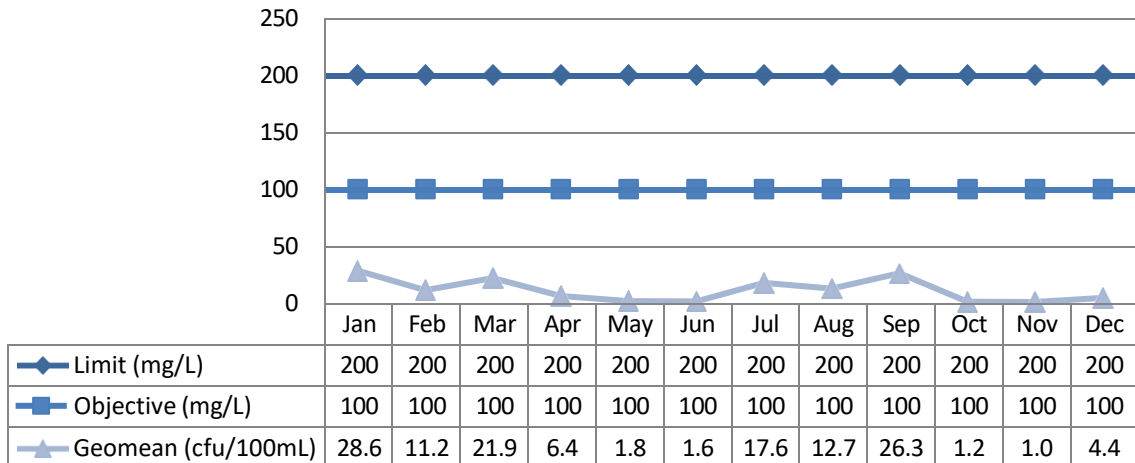


pH

ECA No. 8497-8D3TU7 has a final effluent pH compliance limit within the range of 6.0 to 9.5 and an objective limit within the range of 6.8 - 7.8, inclusive, at all times. The pH of the final effluent ranged from 7.02 – 8.93 throughout 2025 which is within the ECA compliance limit at all times.

Graph 10: Final Effluent Monthly pH Concentration Limit Comparisons for 2025

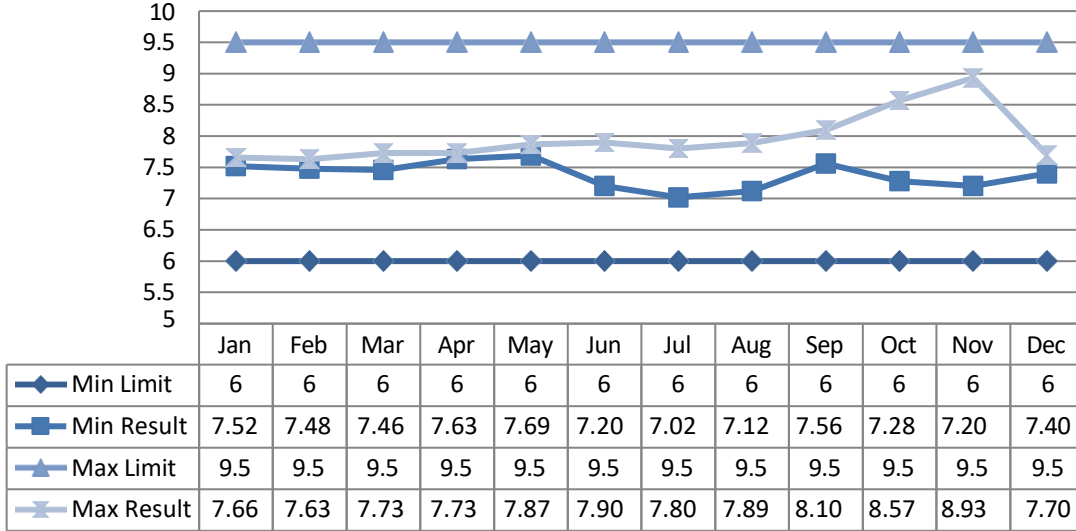

Graph 11: Final Effluent Monthly pH Concentration Objectives Comparisons for 2025

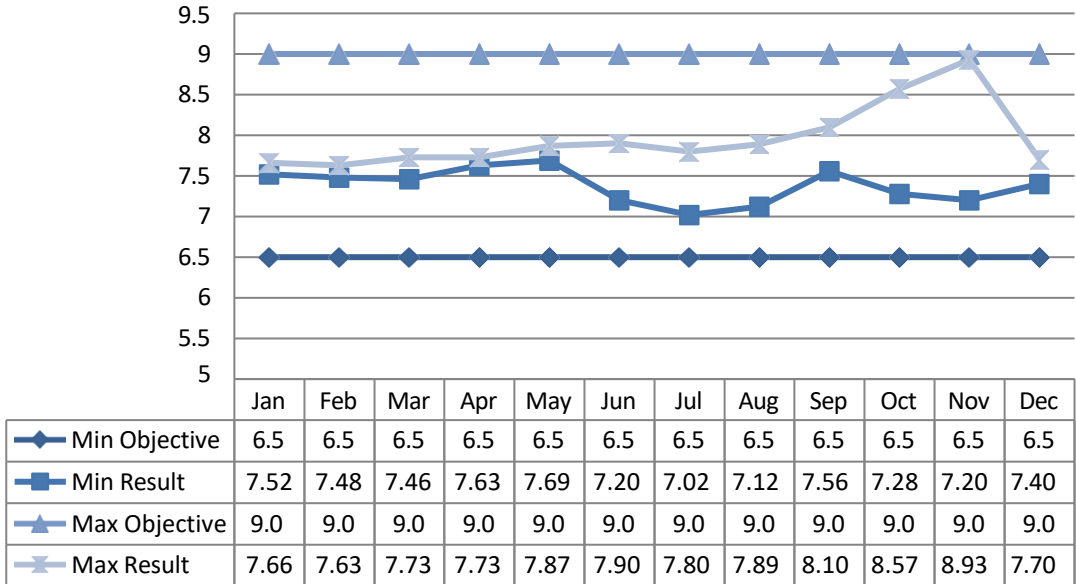

Summary of Septage Received

The Brechin/Lagoon City Wastewater Treatment Plant accepts septage from licensed haulers. A total of 112,075 m3 of septage was received in 2025.

## 7. Description of Operating Problems

ECA #8497-8D3TU7\_Condition 9(5)(b) states that the annual performance report shall contain "a description of any operating problems encountered and corrective actions taken."

The following details describe all operating problems encountered during the reporting period and the corrective actions taken:

TABLE 5: BRECHIN LAGOON CITY WWTP OPERATIONAL CHALLENGES 2025		
Months	Challenges	Corrective Actions
January February March	Elevated flows  Sewage Pumping Station (SPS) #4 generator oil burning  Utility power failures during ice storms	Operational adjustments to accommodate flow  Repaired generator completed following event  Portable Generator utilized at SPS's
April May July	Screw pump drive bearing making noise  SPS 8 Milltronics failed  Plugged sewer on Willow Crescent  Manhole hit by road grader on HWY 12  Waste pump 1 in biosolids pump chamber failed  SPS 7 pump seal failed  Sewer back up at 88 Turtle Path	Inspected and upper bearing replaced in Q3  Replaced Milltronics  Cleared blockage  Repaired manhole  Replaced with spare and sent for repair  Replaced pump installed in Q3  Cleared blockage
July August September	Blocked sewer 19 Turtle Path  Centre aerator bearing failure  Effluent pH sensor faulty	Cleared blockage  Aerator replaced  Replaced pH sensor
October November December	SPS 8 hot water tank failed	Replaced hot water tank

## 8. Summary of Maintenance

ECA No. 8497-8D3TU7 Condition 11(4)(e) states that the annual performance report shall contain *summary of all maintenance carried out on any major structure, equipment, apparatus or mechanism forming part of the Works.*”

Routine maintenance and operation of the Brechin/Lagoon City Wastewater Treatment Plant and Sewage Pumping Stations in 2025 consisted of the following:

- Blew out and restarted return activated sludge siphons
- Changed the oil and filters in the digester blowers
- Cleaned secondary clarifiers
- De-iced mechanical aerators
- Flushed chemical pumps and lines
- Greased bearings of screw conveyor
- Performed routine maintenance and repair of pumps
- Pulled and cleaned or replaced UV bulbs
- Pump Stations Cleaned
- Repaired Clarifier 1 siphons rebuilt
- Replaced Clarifier 1 drive cable
- Installed new Polymer pump
- Added polymer system to essential power
- PS4 multi-ranger replaced
- SPS 7 pump installed
- Screw bearing replaced
- SPS 4 generator serviced
- SPS 3 electrical generator connection replaced
- Annual Calibration completed
- SPS 6 pump serviced and check valves changed
- SPS 5 generator engine anti-freeze leak repaired
- Installed cameras for basin #1 for level monitoring during haulage
- Invert inspects – 3<sup>rd</sup> party
- Repaired spare mixer
- Replaced sump pump impeller
- Replaced UV sensor
- Addition of low-level float for Clarifier basin #1
- High Level/sensor alarming and screw pump speed/level control automation
- Generator Block heater repairs

## 9. Summary of Effluent Quality Assurance or Control Measures

ECA No. 8497-8D3TU7 Condition 9(4)(d) states that the annual performance report shall contain *“a summary of effluent quality assurance or control measures undertaken in the reporting period.”*

Effluent control measures include in-house sampling and testing for operational parameters such as suspended solids, soluble phosphorus, and dissolved oxygen. In-house testing provides real time results which are then evaluated to determine if process changes are necessary to enhance operational performance. All in-house sampling and analysis are performed by certified operations staff utilizing approved methods and

protocols for sampling, analysis and recording as specified in the Ministry’s Procedure F-10-1, “Procedures for Sampling and Analysis Requirements for Municipal and Private Sewage Treatment Works”, the Ministry’s publication, “Protocol for the Sampling and Analysis of Industrial/Municipal Wastewater” and the publication, “Standard Methods for the Examination of Water and Wastewater”.

All final effluent samples collected during the reporting period to meet ECA sampling requirements were submitted to SGS Lakefield Research Ltd. laboratory for analysis, with the exception of pH, temperature and unionized ammonia. SGS Lakefield Research has been deemed accredited by the Canadian Association for Laboratory Accreditation (CALA), meeting strict provincial guidelines including an extensive quality assurance/quality control program. By choosing this laboratory, the Ontario Clean Water Agency is ensuring appropriate control measures are undertaken during sample analysis. The pH and temperature parameters were analyzed in the field at the time of sample collection by certified operators, to ensure accuracy and precision of the results obtained. The unionized ammonia was calculated using the total ammonia nitrogen concentration, pH and temperature as required by the facility Environmental Compliance Approval.

Effluent quality assurance is maintained in several ways. Laboratory samples are sent to an accredited laboratory (SGS Canada Inc. - Lakefield) for analysis of all effluent parameters. Sampling calendars issued to the operator which denote frequency of sampling. Calendars are used as a tracking mechanism throughout the month to ensure all required samples are collected. These calendars are submitted to the Process Compliance Technician at the end of each month for review. Raw and effluent samples are collected as per the Amended Environmental Compliance Approval and the results are reviewed on a regular basis to ensure compliance with the site’s objectives and limits.

Work orders illustrating all scheduled and preventative maintenance to be completed are issued to the operator and/or mechanic. OCWA conducts internal audits of the facility and develops Action Plans to ensure deficiencies are identified.

10. Summary of Calibration and Maintenance

ECA No. 8497-8D3TU7 Condition 9(4)(e) states that the annual performance report shall contain *“a summary of the calibration and maintenance carried out on all effluent monitoring equipment.”*

Calibrations on effluent monitoring equipment were performed by Flowmetrix Technical Services Inc. on April 30, 2025 for equipment located at the Brechin/ Lagoon City Wastewater Treatment Plant. Please see Appendix II: Calibration Reports.

TABLE 6: BRECHIN LAGOON CITY WWTP – SUMMARY OF EQUIPMENT CALIBRATIONS – 2025	
Collection Monitoring Equipment	Date of Completion
Pump Station #4 Flow Meter	April 30, 2025
Pump Station #8 Flow Meter	April 30, 2025
Influent Monitoring Equipment	Date of Completion
Influent Flow Meter	April 30, 2025
Final Effluent Monitoring Equipment	Date of completion
Final Effluent Flow Meter	April 30, 2025
Online pH meter	April 30, 2025

11. Description of Efforts Made and Results Achieved to Meet Effluent Objectives

OCWA uses a number of best efforts to achieve the Effluent Objectives. Effluent quality assurance and control measures include in-house sampling and testing for operational parameters such as suspended solids, phosphorus, dissolved oxygen, etc. In-house testing provides real time results which are then used to enhance process and operational performance. OCWA also collects raw sewage and effluent samples as per the ECA and reviews these results on a regular basis to ensure compliance with the ECA objectives and limits.

OCWA uses a computerized maintenance management system which generates work orders to ensure maintenance of equipment is proactively performed. In addition, OCWA provides regular status reports to the Owner which includes operational data, equipment inventory, financial statements, maintenance activities and capital improvement recommendations.

OCWA has developed comprehensive manuals detailing operations, maintenance, instrumentation and emergency procedures. To ensure facilities are operated in compliance with applicable legal requirements, facility staff have access to a network of operational compliance and support experts at the cluster, region and corporate level.

TABLE 7: EFFORTS MADE TO MEET THE EFFLUENT OBJECTIVES OF CONDITION 9
1. Sampling effluent as per the ECA.
2. Visual Inspection of the effluent while performing rounds.
3. Annual calibration of the pH meter.
4. Annual calibration of the flow meters.
5. Performing preventative maintenance activities in accordance with work order schedules.
6. Monitoring treatment processes through regular in-house checks and review of lab results.
7. Sludge monitoring of primary clarifiers & adjustments to syphon rates based on tank levels to reduce solids carryover.
8. Visual review of microbiological activity of activated sludge to ensure appropriate F/M ratio and control filamentous.

The Brechin/Lagoon City WWTP was able to meet the Effluent Objectives throughout 2025, with the exception of the month of March.

Carbonaceous Biochemical Oxygen Demand (CBOD5)

ECA No. 8497-8D3TU7 sets the final effluent monthly CBOD5 average concentration objective at 8.0 mg/L.

TABLE 8: FINAL EFFLUENT MONTHLY CBOD5 CONCENTRATION OBJECTIVE COMPARISONS 2025			
Monthly Average	Average Concentration (mg/L)	Concentration Objective Target (mg/L)	Objective Achieved
January	4.3	8.0	Yes
February	4.3	8.0	Yes
March	4.0	8.0	Yes
April	4.0	8.0	Yes
May	4.0	8.0	Yes
June	4.0	8.0	Yes
July	4.0	8.0	Yes
August	4.0	8.0	Yes

September	4.0	8.0	Yes
October	4.0	8.0	Yes
November	4.0	8.0	Yes
December	4.0	8.0	Yes

#### Total Suspended Solids (TSS)

ECA No. 8497-8D3TU7 sets the final effluent monthly TSS average concentration objective at 12.0 mg/L.

TABLE 9: FINAL EFFLUENT MONTHLY TSS CONCENTRATION OBJECTIVE COMPARISONS 2025			
Month	Average Concentration (mg/L)	Concentration Objective Target (mg/L)	Objective Achieved
January	5.3	12.0	Yes
February	2.0	12.0	Yes
March	29.0	12.0	No
April	2.4	12.0	Yes
May	2.8	12.0	Yes
June	2.4	12.0	Yes
July	2.0	12.0	Yes
August	2.0	12.0	Yes
September	2.2	12.0	Yes
October	2.0	12.0	Yes
November	2.0	12.0	Yes
December	2.4	12.0	Yes

#### Total Phosphorus (TP)

ECA No. 8497-8D3TU7 sets the final effluent monthly TP average concentration objective at 0.24 mg/L.

TABLE 10: FINAL EFFLUENT MONTHLY TOTAL PHOSPHORUS CONCENTRATION OBJECTIVE COMPARISONS 2025			
Month	Average Concentration (mg/L)	Concentration Objective Target (mg/L)	Objective Achieved
January	0.07	0.24	Yes
February	0.05	0.24	Yes
March	0.37	0.24	No
April	0.03	0.24	Yes
May	0.04	0.24	Yes
June	0.04	0.24	Yes
July	0.04	0.24	Yes
August	0.04	0.24	Yes
September	0.04	0.24	Yes
October	0.03	0.24	Yes
November	0.03	0.24	Yes
December	0.03	0.24	Yes

E. Coli

ECA No. 8497-8D3TU7 sets the final effluent monthly E. Coli geometric mean objective at 100 cfu/100mL.

TABLE 11: FINAL EFFLUENT MONTHLY E. COLI GMD OBJECTIVE COMPARISONS 2025			
Month	Geometric Mean (cfu/100mL)	Concentration Objective Target (cfu/100mL)	Objective Achieved
January	28.6	100	Yes
February	11.2	100	Yes
March	21.9	100	Yes
April	6.4	100	Yes
May	1.8	100	Yes
June	1.6	100	Yes
July	17.6	100	Yes
August	12.7	100	Yes
September	26.3	100	Yes
October	1.2	100	Yes
November	1.0	100	Yes
December	4.4	100	Yes

pH

The pH of the final effluent ranged from 7.02 – 8.93 throughout 2025 which is within the ECA design objectives of 6.50 to 9.00, inclusive, at all times.

TABLE 12: FINAL EFFLUENT MONTHLY pH OBJECTIVE COMPARISONS 2025		
Month	Minimum	Maximum
January	7.52	7.66
February	7.48	7.63
March	7.46	7.73
April	7.63	7.73
May	7.69	7.87
June	7.20	7.90
July	7.02	7.80
August	7.12	7.89
September	7.56	8.10
October	7.28	8.57
November	7.20	8.93
December	7.40	7.70

Unionized Ammonia

The concentration of un-ionized ammonia is calculated using the total ammonia nitrogen, along with field pH and temperature using the methodology stipulated in “Ontario’s Provincial Water Quality Objectives” dated July 1994, as amended. The following are the results for the calculated unionized ammonia.

TABLE 13: WEEKLY FINAL EFFLUENT pH, TEMPERATURE AND CALCULATED UN-IONIZED AMMONIA 2025				
Date	Total Ammonia Nitrogen: NH <sub>3</sub> + NH <sub>4</sub> <sup>+</sup> as N [mg/L]	Field pH	Field temp °C	Un-ionized Ammonia
06/01/2025	0.1	7.62	3.9	0.0005
13/01/2025	0.4	7.55	4.4	0.0017
20/01/2025	0.4	7.58	2.2	0.0015
27/01/2025	3.4	7.53	2.0	0.0112
03/02/2025	4	7.56	1.2	0.0132
11/02/2025	4.8	7.49	2.1	0.0146
18/02/2025	6	7.54	0.5	0.0179
24/02/2025	8.3	7.53	2.5	0.0285
03/03/2025	4.4	7.49	1.7	0.0129
10/03/2025	0.1	7.61	4.4	0.0005
18/03/2025	0.1	7.73	4.2	0.0006
24/03/2025	0.1	7.65	7.0	0.0007
02/04/2025	0.1	7.74	4.0	0.0006
06/04/2025	0.1	7.68	4.5	0.0006
14/04/2025	0.1	7.64	6.5	0.0006
22/04/2025	0.1	7.67	6.5	0.0007
28/04/2025	0.1	7.66	7.6	0.0007
05/05/2025	0.1	7.80	9.0	0.0011
12/05/2025	0.1	7.78	9.7	0.0011
20/05/2025	0.1	7.74	10.0	0.0010
26/05/2025	0.1	7.85	9.8	0.0013
02/06/2025	0.1	7.80	8.1	0.0010
09/06/2025	0.1	7.80	12.4	0.0014
16/06/2025	0.1	7.70	13.2	0.0012
23/06/2025	0.1	7.70	16.7	0.0015
30/06/2025	0.1	7.40	16.1	0.0007
07/07/2025	0.1	7.70	18.2	0.0017
14/07/2025	0.1	7.60	19.4	0.0015
21/07/2025	0.1	7.50	17.7	0.0010
28/07/2025	0.1	7.07	23.1	0.0006
05/08/2025	1.4	7.22	21.6	0.0103
11/08/2025	0.3	7.53	23.5	0.0051
18/08/2025	0.2	7.75	21.3	0.0048

25/08/2025	0.2	7.72	20.8	0.0043
02/09/2025	0.1	7.82	19.3	0.0024
08/09/2025	0.1	7.98	17.6	0.0031
15/09/2025	0.1	7.70	19.5	0.0019
22/09/2025	0.1	7.90	18.9	0.0028
29/09/2025	0.1	7.88	19.2	0.0028
06/10/2025	0.2	7.99	19.3	0.0071
14/10/2025	0.2	8.13	16.4	0.0079
20/10/2025	0.4	8.22	16.6	0.0195
27/10/2025	1.3	8.47	12.7	0.0825
03/11/2025	0.1	8.61	12.7	0.0086
10/11/2025	0.1	8.73	10.8	0.0096
17/11/2025	0.1	8.01	11.1	0.0020
24/11/2025	0.1	7.37	11.4	0.0005
02/12/2025	0.1	7.46	9.3	0.0005
08/12/2025	0.1	7.47	7.8	0.0005
15/12/2025	0.7	7.44	6.7	0.0028
22/12/2025	0.1	7.50	8.1	0.0005
29/12/2025	0.3	7.39	8.3	0.0012

### Temperature

The final effluent temperature ranged from 0.5°C to 23.5°C.

### Additional Parameters

The parameters listed below are collected as per ECA or regulatory requirements or for process optimization.

### Influent Samples

Influent sampling is completed in order to make the necessary process adjustments to stay within the Final Effluent Objectives and limits set in the ECA.

Month	Biochemical Oxygen Demand - BOD5 (mg/L)	Total Suspended Solids – TSS (mg/L)	Total Kjeldahl Nitrogen – TKN (mg/L)	Total Phosphorus – TP (mg/L)
January	63	88	10.4	0.80
February	77	84	15.0	1.39
March	83	98	17.8	1.91
April	34	42	9.3	0.47
May	51	64	12.2	1.15
June	57	63	14.6	1.29
July	157	208	26.2	2.89
August	86	162	21.5	2.13
September	170	197	35.7	3.04

October	95	128	23.3	1.60
November	81	166	15.5	1.55
December	56	66	16.6	1.47

## 12. Summary of Biosolids

The total volume of sludge generated in 2025 was 1432 m<sup>3</sup> which was slightly higher than the amount of sludge generated in 2024. Wessuc Inc. has been contracted to haul, land apply the Biosolids on their approved sites. Monthly sludge samples are collected & tested for metals listed in the Ontario Guidelines for Sewage Biosolids Utilization on Agricultural Lands. There is enough storage to store sludge at the Brechin/ Lagoon City WWTP for the rest of the year.

TABLE 15: MONTHLY SLUDGE GENERATION VOLUMES 2025	
Month	Volume (m <sup>3</sup> )
January	0
February	0
March	0
April	0
May	816
June	0
July	0
August	0
September	0
October	456
November	160
December	0
<b>Total</b>	<b>1432</b>

The anticipated volume of biosolids for the next reporting period is not expected to be significantly different from this reporting period. There are no expected changes in the current sludge handling methods that are currently utilized. Refer to Appendix III: Biosolids Summary

## 13. Summary of Community Complaints

TABLE 16: SUMMARY OF COMPLAINTS 2025		
Date	Issue	Actions Taken
July 4, 2025	Notified by resident of sewage pump on property	Removed pump from property

## 14. Summary of all Bypass, Spill or Abnormal Discharge Events

TABLE 17: SUMMARY OF EVENTS 2025

Date	Type of Event	Total Estimated Volume (m³)	Disinfect (Y/N)	Samples Collected (Y/N)	Reason
March 16, 2025	Bypass	7,235	N	Y	Significant rainfall and snowmelt event causing overwhelming influent volume at treatment facility. Initiated partial bypass of UV system, followed by bypass of basin one to outfall.
April 3, 2025	Bypass	330	N	Y	Significant rainfall event causing overwhelming influent volume at treatment facility. Initiated partial bypass of clarifier and UV system.
May 5, 2025	Sewage Spill	Unknown	N	N	Resident called Township of Ramara to report a sewer backup. OCWA Operator responded to find sewage spilling from residential sewer clean-out onto land and running into municipal ditch. Contacted vac truck to assist with unblocking residential sewer line.

#### 15. Status Update on Initial Effluent Characterization

The initial effluent characterization was submitted as per Condition 8 Section (1). No updates occurred during the reporting period.

#### 16. Additional Information the *District Manager* Requested

The District Manager has not requested any additional information be included in this report.

#### 17. Summary of Efforts Made to Reduce Overflows, Spills and Bypasses

*a) A description of projects undertaken and completed in the Authorized System that result in overall overflow reduction or elimination including expenditures and proposed projects to eliminate overflows with estimated budget forecast for the year following that for which the report is submitted.*

- Efforts to identify and eliminate inflow and infiltration (I&I) sources through CCTV inspections in 2024. The findings of the inspections were to inform budget recommendations to make necessary repairs in 2025 to deficiencies identified.
- An annual budget is allocated to an I&I reduction program.

*b) Details of the establishment and maintenance of a PPCP, including a summary of project progresses compared to the PPCP's timelines.*

- The Ramara Sanitary Sewage Collection system does not contain combined sewers and therefore is not required to complete a Pollution Prevention and Control Plan (PPCP).

*c) An assessment of the effectiveness of each action taken.*

- Nothing to report at this time.

*d) An assessment of the ability to meet Procedure F-5-1 or Procedure F-5-5 objectives (as applicable) and if able to meet the objectives, an overview of next steps and estimated timelines to meet the objectives.*

- Not applicable.

*e) Public reporting approach including proactive efforts.*

- The Township of Ramara utilizes their website and social media platforms to post Media Releases. Residents have the ability to subscribe to receive Media Releases from the Township of Ramara to an email address. The Township of Ramara also distributes a quarterly publication as well as randomized campaigns that bring awareness to the Sewer Use Bylaw and other information related to municipal sewer use such as sump pump connections.

*f) A summary of Alterations to the Authorized System within the reporting period that are authorized by this Approval including a list of Alterations that pose a Significant Drinking Water Threat.*

- No alterations were made to the Authorized System within the reporting period.

# APPENDIX I

Performance Assessment Report




**1617 LAGOON CITY WASTEWATER TREATMENT PLANT 120002255**

	1/ 2025	2/ 2025	3/ 2025	4/ 2025	5/ 2025	6/ 2025	7/ 2025	8/ 2025	9/ 2025	10/ 2025	11/ 2025	12/ 2025	<<-Total-->	<<-Avg-->	<<-Max-->	<<-Criteria-->
<b>Flows</b>																
Raw Flow: Total - Raw m <sup>3</sup> /d	48,390.63	31,506.74	71,893.05	69,744.40	45,937.31	31,987.75	48,859.75	35,142.80	39,505.40	18,603.04	27,285.20	30,348.80	499,204.87			0.00
Raw Flow: Avg - Raw m <sup>3</sup> /d	1,560.99	1,125.24	2,319.13	2,324.81	1,481.85	1,066.26	1,576.12	1,133.84	1,316.85	600.10	909.51	978.99		1,367.68		2,273.00
Raw Flow: Max - Raw m <sup>3</sup> /d	2,327.29	1,727.90	6,159.70	4,729.90	2,318.50	1,780.30	2,820.40	2,007.00	2,339.50	823.40	1,353.30	1,308.40			6,159.70	0.00
Raw Flow: Count - Raw m <sup>3</sup> /d	31.00	28.00	31.00	30.00	31.00	30.00	31.00	31.00	30.00	31.00	30.00	31.00	365.00			0.00
Eff. Flow: Total - Final Effluent m <sup>3</sup> /d	51,983.90	38,006.61	64,659.78	65,431.83	47,006.23	32,514.61	50,139.63	39,193.09	41,379.40	41,474.41	28,502.88	30,809.76	531,102.13			0.00
Eff. Flow: Avg - Final Effluent m <sup>3</sup> /d	1,676.90	1,357.38	2,085.80	2,181.06	1,516.33	1,083.82	1,617.41	1,264.29	1,379.31	1,337.88	950.10	993.88		1,455.07		2,273.00
Eff. Flow: Max - Final Effluent m <sup>3</sup> /d	2,211.27	2,599.30	3,644.89	4,481.68	2,294.67	1,860.30	2,821.34	2,158.59	2,475.89	2,120.98	1,399.50	1,518.17			4,481.68	0.00
Eff. Flow: Count - Final Effluent m <sup>3</sup> /d	31.00	28.00	31.00	30.00	31.00	30.00	31.00	31.00	30.00	31.00	30.00	31.00	365.00			0.00
<b>Carbonaceous Biochemical Oxygen Demand: CBOD</b>																
Eff. Avg cBOD5 - Final Effluent mg/L	< 4.29	< 4.29	< 4.00	< 4.00	< 4.00	< 4.00	< 4.00	< 4.00	< 4.00	< 4.00	< 4.00	< 4.00		< 4.19		10.00
Eff. # of samples of cBOD5 - Final Effluent	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	52.00			0.00
Loading: cBOD5 - Final Effluent kg/d	< 7.127	< 5.769	< 8.343	< 8.724	< 6.065	< 4.335	< 6.470	< 5.057	< 5.517	< 5.352	< 3.800	< 3.974		< 6.10	< 8.72	
<b>Biochemical Oxygen Demand: BOD5</b>																
Raw: Avg BOD5 - Raw mg/L	63.00	77.00	83.00	34.00	51.00	57.00	157.00	86.00	170.00	95.00	81.00	56.00		84.17	170.00	0.00
Raw: # of samples of BOD5 - Raw	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	12.00			0.00
Percent Removal: BOD5 - Raw %	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00		0.00
<b>Total Suspended Solids: TSS</b>																
Raw: Avg TSS - Raw mg/L	88.00	84.00	98.00	42.00	64.00	63.00	208.00	162.00	197.00	128.00	166.00	66.00		113.83	208.00	0.00
Raw: # of samples of TSS - Raw	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	12.00			0.00
Eff. Avg TSS - Final Effluent mg/L	< 5.29	< 2.00	< 29.00	< 2.40	< 2.75	< 2.40	< 2.00	< 2.00	< 2.20	< 2.00	< 2.00	< 2.40		< 4.52	< 29.00	15.00
Eff. # of samples of TSS - Final Effluent	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	52.00			0.00
Loading: TSS - Final Effluent kg/d	< 8.804	< 2.715	< 60.488	< 5.235	< 4.170	< 2.601	< 3.235	< 2.529	< 3.034	< 2.676	< 1.900	< 2.384		< 6.58	< 60.49	
Percent Removal: TSS - Raw %	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00		0.00
<b>Total Phosphorus: TP</b>																
Raw: Avg TP - Raw mg/L	0.80	1.39	1.91	0.47	1.15	1.29	2.89	2.13	3.04	1.60	1.55	1.47		1.64	3.04	0.00
Raw: # of samples of TP - Raw	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	12.00			0.00
Eff. Avg TP - Final Effluent mg/L	0.07	0.05	0.37	< 0.03	0.04	< 0.04	< 0.04	< 0.04	0.04	< 0.03	< 0.03	< 0.03		0.05	0.37	0.30
Eff. # of samples of TP - Final Effluent	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	52.00			0.00
Loading: TP - Final Effluent kg/d	0.113	0.068	0.761	< 0.065	0.057	< 0.039	< 0.069	< 0.047	0.061	< 0.040	< 0.037	< 0.032		0.14	0.76	249.000
Percent Removal: TP - Raw %	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00		0.00
<b>Nitrogen Series</b>																
Raw: Avg TKN - Raw mg/L	10.40	15.00	17.80	9.30	12.20	14.60	26.20	21.50	35.70	23.30	15.50	16.60		18.16	35.70	0.00
Raw: # of samples of TKN - Raw	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	12.00			0.00
Eff. Avg TAN - Final Effluent mg/L	< 1.08	< 5.78	< 1.18	< 0.10	< 0.10	< 0.10	< 0.30	< 0.53	< 0.10	< 0.53	< 0.10	< 0.26		< 0.85	< 5.78	
Eff. # of samples of TAN - Final Effluent	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	52.00			0.00
Loading: TAN - Final Effluent kg/d	< 1.803	< 7.839	< 2.451	< 0.218	< 0.152	< 0.108	< 0.485	< 0.664	< 0.138	< 0.702	< 0.095	< 0.258		< 1.24	< 7.84	
Eff. Avg NO3-N - Final Effluent mg/L	9.16	6.08	7.58	6.76	11.09	15.92	17.15	17.83	16.04	12.46	13.13	12.54		12.14	17.83	0.00
Eff. # of samples of NO3-N - Final Effluent	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	52.00			0.00
Eff. Avg NO2-N - Final Effluent mg/L	0.29	< 0.06	< 0.05	< 0.05	< 0.08	< 0.22	< 0.08	< 0.07	< 0.04	1.56	0.19	0.76		< 0.29	1.56	0.00
Eff. # of samples of NO2-N - Final Effluent	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	52.00			0.00
<b>Disinfection</b>																
Eff. GMD E. Coli MPN - Final Effluent MPN	28.55	11.23	21.91	6.35	1.86	1.55	17.84	12.70	26.30	1.19	1.00	4.44				0.00
Eff. # of samples of E. Coli MPN - Final Effluent	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	4.00	52.00			0.00

# APPENDIX II

Calibration Reports





**FLOWMETRIX**  
TECHNICAL SERVICES

# **FLOW, PRESSURE and WATER QUALITY INSTRUMENTATION**

**Verification/Calibration**

## **REPORT**

# **OCWA**

 **ONTARIO CLEAN WATER AGENCY**  
**AGENCE ONTARIENNE DES EAUX**

**- KAWARTHA LAKES – RAMARA TWP -**

**APRIL/MAY 2025**

May 22<sup>nd</sup>, 2025

Ontario Clean Water Agency  
Kawartha Lakes  
Rob Smith  
Team Lead  
123 East St. S  
Bobcaygeon ,ON K0M 1A0  
T: 705-623-7273  
E: [RSmith@ocwa.com](mailto:RSmith@ocwa.com)

---

**RE: Annual Verification/Calibration for the Township of Ramara  
WWTP - AC & WQA  
April 30th & May 1st, 2025**

---

Dear Rob,

SCG Flowmetrix appreciates the opportunity to complete your field service and verification/calibration services. This letter of transmittal confirms completion of this service project.

The following service report contains the individual instrument reports for all verification/calibrations as well as an Equipment List Summary.

***Note: Equipment List Summary is only included where 5 or more instruments are verified/calibrated for the same client/area. Otherwise, only individual reports are provided.***

In addition to the base report, relevant information related to standard approach and methodologies for various instruments verified and/or calibrated, and a statement of qualifications for all verification/calibrations completed by trained, knowledgeable and experienced personnel is found in the section Quality Assurance and Quality Control.

If you have any additional questions or concerns with regards to this report, please do not hesitate to contact me directly.

Kind Regards,

*Sarah Cawston*

Sarah Cawston  
Sales & Service Coordinator  
2088 Jetstream Rd.  
London, ON N5V 3P6  
c. 519-281-9660  
[scawston@scgflowmetrix.com](mailto:scawston@scgflowmetrix.com)

## QUALITY ASSURANCE/QUALITY CONTROL

Flowmetrix adheres to a rigid scope of service and deliverables for each client and instrument verified, calibrated, and reported. We follow a standard guideline while performing verification and calibration procedures for each instrument, using original equipment manufacturer (OEM) tools, where possible. The values are field reported and entered in a standard report format for client review. A digital report is completed for each instrument and collated into a single document for client record.

### Approach & Methodology

Flowmetrix conducts verification of each instrument and subsequent calibrations on instruments that are outside the expected tolerance of the instrument response, where possible. Manufacturers OEM suggested testing guidelines are used to verify and/or calibrate each instrument. Where, unable to perform the verification or calibration as suggested by the manufacturer, a best management practice is performed to validate the performance of such instruments.

### **REPORTING**

Flowmetrix report is divided into (2) sections. Section (i) identifies an equipment summary of all instruments verified during this service project including instruments that PASS or FAIL; section (ii) identifies individual equipment reports for client review and record and identifies any comments and deficiencies that should be noted for client review and possible response.

#### Section (i) - Equipment Summary

An equipment summary sheet identifying all instruments; both PASSING and FAILING verification and/or calibration while completed during this service project.

The Summary Equipment List is only included where 5 or more instruments are verified/calibrated for the same client/area. Otherwise, only individual reports are provided.

#### Section (ii) - Individual Equipment Reports

Individual equipment reports are completed for easy review and are found in Appendix B. These reports outline all specific information pertaining to the equipment be tested; noted as meter under test (MUT). Date, time, location, meter make, model and serial number accompany this report for tracking and identification. Each report identifies a PASS or FAIL comment 'as found' and 'as left' upon completion of the verification and/or calibration.

Where possible, a verification is performed prior to calibration, if the OEM testing procedures allow, otherwise an 'as left' report is provided for such equipment.

**Note: If a meter under test (MUT) is (AS FOUND) to be operating outside of the allowable tolerance, the report will indicate "NA". The "NA" statement is NOT suggesting the MUT, or a component of the MUT is not functional or has failed; but simply indicates at the time the test was conducted the verification reported values are found outside the allowable tolerance.**

**Only if the MUT is failed due to equipment failure and not verification/calibration tolerances, the report will indicate "FAIL" (AS FOUND) and will be commented on in the individual equipment report.**

### **STATEMENT OF QUALIFICATIONS**

To comply with our clients DWQMS standards, Flowmetrix adheres to a rigid approach to conducting our equipment verification/calibration services including the training received by our company and our personnel conducting service. A Statement of Qualifications outlining Flowmetrix qualifications to conduct this level of service is available in a separate document upon request.



**A P P E N D I X - B**  
INDIVIDUAL INSTRUMENT REPORTS

### AS FOUND CERTIFICATION

### FORWARD FLOW DIRECTION

### PASS

#### CLIENT DETAIL

CUSTOMER OCWA – Kawartha Lakes Hub  
 CONTACT Nick Leroux  
 Senior Operations Manager  
 123 East St S  
 Bobcaygeon ON, K0M 1A0  
 P: 705-623-7278  
 E: nleroux@ocwa.com

#### EQUIPMENT DETAIL

[MUT] MANUFACTURER Rosemount  
 MODEL 8712  
 CONVERTER SERIAL NUMBER 08060245142  
 PLANT ID Lagoon City STP  
 METER ID Final Effluent Flow  
 FIT ID NA  
 CLIENT TAG 0000336599  
 OTHER NA  
 GPS COORDINATES N 44°33.467 W 079°12.436

VER. BY - FM Daniel Kettlewell  
 Quality Management Standards Information -

Reference equipment and instrumentation used to conduct this verification test is found in our AC-QMS document at the time this test was conducted.

VERIFICATION DATE April 30th 2025  
 CAL. FREQUENCY Annual  
 CAL. DUE DATE April 2026

#### PROGRAMMING PARAMETERS

DIAMETER (DN) mm 300  
 F.S. FLOW - MAG LPS 859.000  
 F.S. RANGE - O/P LPS 600.000

#### FORWARD TOTALIZER INFORMATION

AS FOUND 1012750 M3  
 AS LEFT 1012819 M3  
 DIFFERENCE 69 M3

TUBE CAL. FACTOR 1108905010807005

#### TEST CRITERIA

AS FOUND CERTIFICATION TEST Yes  
 FORWARD FLOW DIRECTION Yes  
 ALLOWABLE [%] ERROR 5

VERIFICATOR CAL. FACTOR 1000015010000000  
 [16-digits]

#### COMPONENTS TESTED

CONVERTER DISPLAY yes  
 mA OUTPUT yes  
 TOTALIZER yes  
 ACCURACY BASED ON [% o.r.] yes  
 ERROR DOCUMENTED IN THIS REPORT; BASED ON % o.r.

#### FLOW TUBE SIMULATION

	0	3	10	30	ft/s
<b>DISPLAY</b>	0.00	3.00	10.00	30.00	ft/s
MUT Reading	0.00	3.00	10.00	30.00	ft/s
MUT % Error	n/a	0.00	0.00	0.00	%
<b>mA OUTPUT</b>	4.000	5.600	9.333	20.000	mA
MUT Reading	4 mA	5.602	9.343	20.026	mA
MUT % Error	20 mA	0.04	0.10	0.13	%
<b>TOTALIZER</b>				30.00	ft/s
TEST Accumulation				2000.00	ft
TIME				66.54	seconds
CALC. Velocity				30.06	ft/s
% Error				0.19	%

#### QUALITY MANAGEMENT STANDARDS INFO.

[QMS] INFORMATION	IDENT.	ID #
[REFERENCE] FTS	ROS	1
PROCESS METER	PM	0
ANALOG METER	AM	n/a
STOP WATCH	SW	Yes

\*All values are for "As Found" values.

COMMENTS	RESULTS		
	TEST	AVG % o.r.	PASS FAIL

DISPLAY	0.00	PASS
mA OUTPUT	0.09	PASS
TOTALIZER	0.19	PASS

---

This report reflects the test results of the overall accuracy for the above flow converter using the specified manufacturers flow tube simulator to within the specified tolerance as identified within this report.

**AS FOUND CERTIFICATION**

**PASS**

**CLIENT DETAIL**

CUSTOMER OCWA – Kawartha Lakes Hub  
CONTACT Nick Leroux  
Senior Operations Manager  
123 East St S  
Bobcaygeon ON, K0M 1A0  
P: 705-623-7278  
E: nleroux@ocwa.com

[MUT] MANUFACTURER Greyline  
MODEL OCF-IV  
CONVERTER SERIAL NUMBER 17849

PLANT ID Lagoon City  
METER ID Influent Flow  
FIT ID NA  
CLIENT TAG 0000334212  
OTHER NA  
GPS COORDINATES N 44°33.467 W 079°12.436

VER. BY - FM Daniel Kettlewell

Quality Management Standards Information -  
Reference equipment and instrumentation used to  
conduct this verification test is found in our AC-QMS  
document at the time this test was conducted.

VERIFICATION DATE April 30th 2025  
CAL. FREQUENCY Annual  
CAL. DUE DATE April 2026

**PROGRAMMING PARAMETERS**

NOTCH ANGLE (φ)	inches	45
EMPTY DISTANCE, TX to notch	m	0.662
TRANSDUCER (TX), to sump fl	m	0.78
SUMP LEVEL, zero flow	m	0.118
MAX. HEAD	m	0.300
BLANKING DISTANCE	m	0.362
DEAD ZONE	m	0.000
MAX. FLOW	M3/H	101.4
F.S. RANGE - O/P	M3/H	101.4

**TOTALIZER**  
AS FOUND 217488 M3  
AS LEFT 217490 M3  
DIFFERENCE 2 M3  
AS FOUND CERTIFICATION TEST  
ALLOWABLE [%] ERROR **TEST CRITERIA**

Yes  
15

**COMPONENTS TESTED**

CONVERTER DISPLAY yes  
mA OUTPUT yes  
TOTALIZER no  
ACCURACY BASED ON [% o.r.] yes

ERROR DOCUMENTED IN THIS REPORT; BASED ON % o.r.

Ultrasonic Sensor is not installed high enough, to ensure full scale flow conditions

**AS FOUND TEST RESULTS**

		0.0	3.1	17.7	48.7	100.0	% F.S. Range
		0.000	0.075	0.150	0.225	0.300	m
<b>REF. FLOW RATE</b>		<b>0.0</b>	<b>3.2</b>	<b>17.9</b>	<b>49.4</b>	<b>101.4</b>	M3/H
MUT [Reading]		0.0	3.2	17.9	48.7	101.8	M3/H
MUT [Difference]		0.0	0.0	0.0	-0.7	0.4	M3/H
MUT [% Error]		0.0	1.0	-0.1	-1.4	0.4	%
<b>mA OUTPUT</b>		<b>4.000</b>	<b>4.500</b>	<b>6.828</b>	<b>11.794</b>	<b>20.000</b>	mA
MUT [Reading]	min. 4.000 mA	4.000	4.516	6.852	11.619	20.002	mA
MUT [Difference]	max. 20.000 mA	0.000	0.016	0.024	-0.175	0.002	mA
MUT [% Error]		0.00	0.36	0.35	-1.49	0.01	%
<b>TOTALIZER - REF. FLOW RATE</b>							
TOTALIZER [MUT]							
TEST TIME							
CALC. TOTALIZER							
ERROR							

**COMMENTS**

-Results based on Internal Simulation not actual flow.

**QUALITY MANAGEMENT STANDARDS INFO.**

[QMS] INFORMATION	IDENT.	ID #
[REFERENCE] LEVEL	Sim. BOARD	n/a
PROCESS METER	PM	0
STOP WATCH	SW	n/a

**RESULTS**

TEST	AVG % o.r.	PASS FAIL
DISPLAY	-0.04	PASS
mA OUTPUT	-0.15	PASS
TOTALIZER	N/A	N/A



# v-Notch Weir Verification/Calibration Report

This report reflects the test results of the meter's accuracy for the above flow converter using the specified manufacturer's flow tube simulator to within the specified tolerance as identified within this report.

## VeriMas1,er - Flow Meter Verification Report

Customer Information	Meter Information
<b>Customer</b> OCWA Ramarn <b>Verification Date</b> Wed, Apr 30, 2025	<b>Meter Owner</b> PS4 <b>Meter Type</b> WaterMaster <b>Sensor Size</b> DN200 <b>Pipe Status</b> Fluid Present <b>Sensor Type</b> Filt. Inflow <b>Sensor Serial No</b> 3K220000196136 <b>Transmitter Serial No</b> 3K220000382532 <b>Tag1</b> FIT-SPS#4 <b>Location</b>

**Overall Status: Pass**

The flowmeter has passed its internal, continuous verification and automatic self-calibration. It is working within +/- 1% of its original factory calibration.

Summary of Results	Verification History
<b>Electrode Group</b> Passed <b>Electrode Group</b> Passed <b>Sensor Group</b> Passed <b>Transmitter Signal</b> Passed <b>Transmitter Driver</b> Passed <b>Output Group</b> Passed <b>Configuration</b> Passed	<b>Verification History</b> 11/11/2025 <b>Accuracy Alarms</b> 0
<b>Sensor Information</b> QI- 1000.00 m3/h Calibration Accuracy OIML Class2 Sensor Calibration Factors 113.8%; -0.55 mm/s; 11 Date of Manufacture 2016 Oct 17 Run Hours 3492days19hrs55mins	<b>Flow Information</b> <b>Forward</b> 362977.50 m3 <b>Reverse</b> 416.85 m3 <b>Net</b> 3620457.26 m3
<b>Transmitter Information</b> Application Version VOI JJ6.00 03/03/15 MSP Version 01.00.00 Date of Manufacture 2016 Oct 17 Run Hours 4648days19hrs45mins	<b>Sensor Data</b> Coil Current 179.9 mA Coil Resistance 99.6 mH Coil Inductance -0.5% Coil/Loop Resistance 31.8 ohm
<b>Current Output</b> 4mA Value Pass: 4.000 mA; 0.00% 12mA Value Pass: 11.983 mA; 0.14% 20mA Value Pass: 19.990 mA; 0.04%	<b>Transmitter Data</b> Tx Frequency Adjustment 0.0%
	<b>VeriMas1,er Information</b> Version 01.00.03 Limit Version 01.00.01
	<b>Pulse Output</b> Output 1: 100.0Hz Not tested Output 2: 50.0Hz Not tested Output Z: 100.0Hz Not tested Output Z: 50.0Hz Not tested

Installation Comments / Equipment:	Configuration Settings
OMM-01 used for mA011.1tp11.1t check	<b>Measurement Frequency</b> 50 Hz <b>Qmax</b> 1000.00 m3/h <b>Pulses/Unit</b> 50.000000 <b>Pulses Limit Frequency</b> 100.0 Hz <b>Sensor User Span/Zero</b> -100.0%; 0.00 mm/s <b>User Flow Offset/Hysteresis</b> 0.00%; 20% <b>Meter Mode</b> Forward Flow

Date: Wed, Apr 30, 2025      Operator: [Signature]      Print

ABH Australia Pty Ltd Bapaune  
R. dl **Moorebank, Nr S, W** 2170 1  
el: +61-2\_-;9821-0111 Fax: +61-  
2\_-;9821-0950

AB, B, Aurtomatoo 6 mbH  
Drameldler Str 2  
3.71079 '6ott"Rg, en, 6 ERMANY  
l el: +4 9 (0) 551 905, 212  
Fax: +1 (215) '674 63-94

**AS FOUND CERTIFICATION**
**FORWARD FLOW DIRECTION**
**PASS**
**CLIENT DETAIL**

CUSTOMER OCWA – Kawartha Lakes Hub  
 CONTACT Nick Leroux  
 Senior Operations Manager  
 123 East St S  
 Bobcaygeon ON, K0M 1A0  
 P: 705-623-7278  
 E: nleroux@ocwa.com

[MUT] MANUFACTURER Krohne  
 MODEL IFC 300  
 SERIAL NUMBER A08 03059  
 FUSE Lighting Panel #14  
 PLANT ID Brechin Community Park  
 METER ID Pump Station #08  
 FIT ID N/A  
 CLIENT TAG N/A  
 OTHER N/A  
 GPS COORDINATES N 44°32.760 W 079°10.769

**EQUIPMENT DETAIL**

VER. BY - FM Daniel Kettlewell

Quality Management Standards Information -  
 Reference equipment and instrumentation used to  
 conduct this verification test is found in our AC-  
 QMS document at the time this test was  
 conducted.

VERIFICATION DATE April 30th 2025  
 CAL. FREQUENCY Annual  
 CAL. DUE DATE April 2026

**PROGRAMMING PARAMETERS**

DIAMETER (DN) mm 150  
 F.S. FLOW - MAG LPS 160.1  
 F.S. RANGE - O/P LPS 60.000  
 CAL. k-FACTOR GK 2.97280

**FORWARD TOTALIZER INFORMATION**

AS FOUND 60039.2 M3  
 AS LEFT 60047.1 M3  
 DIFFERENCE 7.9 M3

**TEST CRITERIA**

AS FOUND CERTIFICATION TEST Yes  
 FORWARD FLOW DIRECTION Yes  
 ALLOWABLE [%] ERROR 15

**COMPONENTS TESTED**

CONVERTER DISPLAY yes  
 mA OUTPUT yes  
 TOTALIZER Yes  
 ACCURACY BASED ON [% o.r.] yes  
 ERROR DOCUMENTED IN THIS REPORT; BASED ON % o.r.

Zero Offset Flow LPS 0.0000

**FLOW TUBE SIMULATION**

		0.0	0.5	1.0	2.0	m/s
		0.0	5.0	10.0	20.0	% F.S. Flow
		0.0	13.3	26.7	53.4	% F.S. Range
<b>REF. FLOW RATE</b>		<b>0.000</b>	<b>8.01</b>	<b>16.01</b>	<b>32.02</b>	LPS
MUT [Reading]		0.000	8.0	16.1	32.0	LPS
MUT [Difference]		0.000	-0.006	0.088	-0.025	LPS
MUT [% Error]		n/a	-0.08	0.55	-0.08	%
<b>mA OUTPUT</b>		<b>4.000</b>	<b>6.135</b>	<b>8.270</b>	<b>12.540</b>	mA
MUT [Reading]	min. 4.000 mA	4.006	6.139	8.271	12.541	mA
MUT [Difference]	max. 20.000 mA	0.006	0.004	0.001	0.001	mA
MUT [% Error]		0.15	0.07	0.01	0.01	%
<b>TOTALIZER - REF. FLOW RATE</b>					<b>32.025</b>	LPS
TOTALIZER [MUT]					2.20	M3
TEST TIME					68.44	SECONDS
CALC. TOTALIZER					2.192	M3
ERROR					0.37	%

**COMMENTS**
**QUALITY MANAGEMENT STANDARDS INFO.**

[QMS] INFORMATION IDENT. ID #  
 [REFERENCE] FTS KRO 1  
 PROCESS METER PM 0  
 ANALOG METER AM N/A  
 STOP WATCH SW YES

**RESULTS**

TEST	AVG % o.r.	PASS FAIL
DISPLAY	0.13	PASS
mA OUTPUT	0.06	PASS
TOTALIZER	0.37	PASS

This report reflects the test results of the overall accuracy for the above flow converter using the specified manufacturers flow tube simulator to within the specified tolerance as identified within this report.



RESULTS **PASS**

CUSTOMER OCWA – Kawartha Lakes Hub  
 CONTACT Nick Leroux  
 Senior Operations Manager  
 123 East St S  
 Bobcaygeon ON, K0M 1A0  
 P: 705-623-7278  
 E: nleroux@ocwa.com

[MUT] MANUFACTURER ABB  
 MODEL AX460/600010/STD  
 SERIAL NUMBER 3K22000652669  
 CLIENT TAG 0000336600  
 LOCATION Lagon City STP  
 OTHER Final Effluent Flow  
 GPS COORDINATES N 44°33.467 W 079°12.436

VER. BY Daniel Kettlewell

TOLERANCE [pH] 0.1

Quality Management Standards Information -  
 Standards, reference equipment, and

VERIFICATION DATE April 30th 2025

instrumentation used to conduct this test outlining  
 the lot#, and expiry date is found in our current

CAL. FREQUENCY Annual  
 CAL. DUE DATE April 2026

**pH VERIFICATION**  
**NIST TRACEABLE (BUFFERS)**

BEFORE CALIBRATION

REFERENCE BUFFER			[MUT] READINGS			
pH BUFFER	TEMP. °C	pH CORRECTED	pH	TEMP. °C	pH - ERROR DIFF.	PASS FAIL
4.01	8.0	4.00	4.20	8.0	0.20	FAIL
7.01	8.1	7.07	7.52	8.1	0.45	FAIL
					<b>RESULT</b>	<b>FAIL</b>

AFTER CALIBRATION

REFERENCE BUFFER			[MUT] READINGS			
pH BUFFER	TEMP. °C	pH CORRECTED	pH	TEMP. °C	pH - ERROR DIFF.	PASS FAIL
4.01	8.0	4.00	4.00	8.0	0.00	PASS
7.01	8.1	7.07	7.01	8.1	-0.06	PASS
					<b>RESULT</b>	<b>PASS</b>

**COMMENTS**

Slope: 102.6%

[QMS] INFORMATION

ITEM

ID #

[REFERENCE]

4.01 BUFFER	pHBUFF4	1
7.01 BUFFER	pHBUFF7	1
TEMPERATURE REF.	DDTEMP	1

NIST Traceable Buffers were used to confirm the overall accuracy of this instrument. "AS FOUND" readings and "AS FOUND" readings are reported within this report. A temperature device was used to measure and record the buffer temperature to correct for pH values due to the effects related to buffer temperature.

# PASS

<b>CUSTOMER CONTACT</b> OCWA – Kawartha Lakes Hub Nick Leroux Senior Operations Manager 123 East St S Bobcaygeon ON, K0M 1A0 P: 705-623-7278 E: nleroux@ocwa.com	<b>[MUT] MANUFACTURER</b> HACH <b>MODEL</b> HQ40D <b>SERIAL NUMBER</b> N/A <b>CLIENT TAG</b> 0000334246 <b>LOCATION</b> Lagoon City WWTP <b>OTHER</b> n/a
---	--

<b>VER. BY</b> Daniel Kettlewell	<b>TOLERANCE [pH]</b> 0.05
-------------------------------------	-------------------------------

Quality Management Standards Information - Standards, reference equipment, and instrumentation used to conduct this test outlining the lot#, and expiry date is found in our current	<b>VERIFICATION DATE</b> April 30th 2025 <b>CAL. FREQUENCY</b> Annual <b>CAL. DUE DATE</b> April 2026
---	--

**AS FOUND**

DO Concentration [mg/L]	9.04
DO Concentration [%]	101
Barometric Pressure [hpa]	19.4
Temperature	985

**AS LEFT**

DO Concentration [mg/L]	9.45
DO Concentration [%]	100
Barometric Pressure [hpa]	985
Temperature	16.7

**COMMENTS**
[QMS] INFORMATION
ITEM
ID #

Calibration performed as per manufacturer's recommended procedure.

NIST Traceable Buffers were used to confirm the overall accuracy of this instrument. "AS FOUND" readings and "AS FOUND" readings are reported within this report. A temperature device was used to measure and record the buffer temperature to correct for pH values due to the effects related to buffer temperature.

# PASS

**AS FOUND CERTIFICATION**

<b>CUSTOMER CONTACT</b>	OCWA – Kawartha Lakes Hub Nick Leroux Senior Operations Manager 123 East St S Bobcaygeon ON, K0M 1A0 P: 705-623-7278 E: nleroux@ocwa.com	<b>[MUT] MANUFACTURER MODEL SERIAL NUMBER CLIENT TAG LOCATION OTHER</b>	HACH DR900 222646601030 n/a Lagoon City WWTP n/a
-------------------------	--	---	---

<b>VER. BY</b>	<i>Daniel Kettlewell</i>	<b>TOLERANCE [mg/L]</b>	0.05
		<b>STANDARD RECOVERY [%]</b>	90
Quality Management Standards Information - Standards, reference equipment, and instrumentation used to conduct this test outlining the lot#, and expiry date is found in our current QMS document.		<b>VERIFICATION DATE</b>	April 30th 2025
		<b>CAL. FREQUENCY</b>	Annual
		<b>CAL. DUE DATE</b>	April 2026

**CHLORINE [Cl<sub>2</sub>] SECONDARY STANDARDS**

STANDARD	BLANK [mg/L]			READING mg/L	PASS FAIL
		+/-			
STD 1	0.18	+/-	0.09	0.20	PASS
STD 2	0.86	+/-	0.10	0.86	PASS
STD 3	1.57	+/-	0.14	1.59	PASS

**CHLORINE [Cl<sub>2</sub>] PRIMARY STANDARDS**

<b>STANDARD VALUE [mg/L]</b>	25.77	<b>BLANK SAMPLE SIZE [mL]</b>	10.0
<b>STANDARD ADDITIONS SIZE [mL]</b>	0.200		
		<b>DPD LOT#</b>	A2315
		<b>EXPIRY DATE</b>	Nov-27

SAMPLE TEST #	Cl <sub>2</sub> STANDARD mL	COMBINED SAMPLE mL	REFERENCE STANDARD mg/L	REFERENCE READING mg/L	MUT READING mg/L	DIFF. ERROR mg/L	PASS FAIL	STANDARD RECOVERY %
BLANK	0	10.000	0	0	0	0	PASS	N/A
STD 1	0.200	10.200	0.51	0.56	0.52	-0.04	PASS	109.8
STD 2	0.400	10.400	0.99	1.06	1.01	-0.05	PASS	107.1
STD 3	0.600	10.600	1.46	1.49	1.44	-0.05	PASS	102.1
<b>AVERAGE RESULTS</b>						-0.05	PASS	106.3

<b>COMMENTS</b>	<b>[QMS] INFORMATION</b>	<b>ITEM</b>	<b>ID #</b>
	[REFERENCE] HACH PCII	HACH PC II	1
	10.0 mL PIPETTE	HACH-PP-10	1
	0.2 mL PIPETTE	G-PP-2	1
	SECONDARY STANDARDS	AS-CLSS	1
	PRIMARY STANDARDS	AS-CLPS	1
	ABSORBANCE STANDARDS	AS-ABS	1

ABSORBANCE CHECKS		
WAVELENGTH	TESTED	PASS/FAIL
420 nm	Yes	PASS
520 nm	Yes	PASS
560 nm	Yes	PASS
610 nm	Yes	PASS

Primary and Secondary standards were used to confirm the overall accuracy of this instrument along with conducting an analytical comparative technique against a reference meter. All values are considered "AS FOUND" readings. If the "AS FOUND" readings were not within acceptable limits, an "AS LEFT" report will be issued if the instrument was able to be calibrated to indicate the overall accuracy of the meter. If the meter was not calibrated for any reason, a comment will be issued for this instrument.



ABB MEASUREMENT & ANALYTICS | TEST REPORT

# ABB Ability™

## Verification for measurement devices



### Verification Report for: WaterMaster

**Measurement made easy**

—  
Measurement & Analytics  
Service

#### Installation Details

Meter Owner

Machine Name

Medium

#### Operator Details

Date and Time 30-05-2024 11:48:23

Operator's Name Admin

Operator's Signature

#### Customer Details

Site Address Lagoon City WWTP

Telephone

Email

## Overall Status - Passed

The flowmeter has passed its internal continuous verification and automatic self-calibration. It is working within +/- 2% of original factory calibration.

ABB Ability Verification for measurement devices verifies the function of the measurement product within the specification limits over the lifetime of the device with a total test coverage > 90% and complies with the requirements for traceable verification according to DIN EN ISO 9001:2015 - section 8.5

### Sensor Information

Sensor Serial No.	5015506
Sensor SAP/ERP No.	3K220000167646
Sensor Type	WM Full Bore
Sensor Size	DN 50
Q3	35.000 l/s
Calibration Accuracy	OIML Class 2
Sensor Calibration Factors	176.738 %, -0.820 mm/s
Date of Manufacture	11:23:51 2013/01/07
Sensor User Span/Zero	100.000 %, 8.998 mm/s
User Flow Cutoff/Hysteresis	0.000 %, 20.000 %
Coil Current	180.000 mA
Coil Inductance	20.240 mH
Coil / Loop Resistance	28.501 Ohm

### Summary Verification of the Sensor

#### Summary of Results

Coil Group	PASS
Electrode Group	PASS
Sensor Group	PASS
Transmitter Signal	PASS
Transmitter Driver	PASS
Configuration	PASS

#### Sensor Data

Coil Inductance Shift	-0.3 %
Cable Length	0 m
Electrode Backoff Voltage	-0.104 V
Electrode Differential Voltage	0.018 V

#### Pipe Status

**Full Pipe**

### Transmitter Information

Transmitter Serial No	34160
Transmitter SAP/ERP No.	3K220000167646
Application Version	V01.05.00 12/07/12
MSP Version	00.00.04
Date of Manufacture	13:46:51 2012/11/15
Tx Gain Adjustment	0.020 %
OIML Accuracy Alarms	OFF
Mains Freq	60.000 Hz
Qmax	35.000 l/s
Pulses/Unit	1.000
FS Freq	35.000 Hz
Pulses Limit Freq	16.667 Hz
Meter Mode	Forward Only

### Summary Verification of the Transmitter

#### Output Group

#### Current Output 31/32

**PASS**

Applied	Measured	Result
4 mA	3.990 mA	PASS
12 mA	11.971 mA	PASS
20 mA	19.982 mA	PASS

#### Pulse Output 41/42

**NOT EXECUTED**

Applied	Measured	Result
5250 Hz		
2625 Hz		

#### Pulse Output 51/52

**NOT EXECUTED**

Applied	Measured	Result
5250 Hz		
2625 Hz		

### Totalizer Information

	Start	End	Difference
Forward	278004511 l	278004511 l	0.000 l
Reverse	19.800 l	19.800 l	0.000 l
Net	278004511 l	278004511 l	0.000 l

## Comments (Installation, Grounding etc.)

---

Verified current using DMM-0

---

Verification Certificate has been generated by ABB Ability Verification for measurement devices variant "Licensed software testing" (ABB WaterMaster VDF Version 03.34).

ABB Ability Verification for measurement devices Version 04.00.00.7

—  
To find your local ABB contact, visit:

**[abb.com/contacts](http://abb.com/contacts)**

For more information, visit:

**[abb.com/measurement](http://abb.com/measurement)**

—  
We reserve the right to make technical changes or modify the contents of this document without prior notice. With regard to purchase orders, the agreed particulars shall prevail. ABB does not accept any responsibility whatsoever for potential errors or possible lack of information in this document. We reserve all rights in this document and in the subject matter and illustrations contained therein. Any reproduction, disclosure to third parties or utilization of its contents – in whole or in parts – is forbidden without prior written consent of ABB.

For further details regarding ABB's warranties arising from the usage of the information including by you or any third party please refer to the Agreement.  
Copyright© 2022 ABB

### AS FOUND CERTIFICATION

**PASS**

#### CLIENT DETAIL

CUSTOMER OCWA – Kawartha Lakes Hub  
 CONTACT Nick Leroux  
 Senior Operations Manager  
 123 East St S  
 Bobcaygeon ON, K0M 1A0  
 P: 705-623-7278  
 E: nleroux@ocwa.com

#### EQUIPMENT DETAIL

[MUT] MANUFACTURER Siemens  
 MODEL LT500  
 CONVERTER SERIAL NUMBER PBD-R7100002  
 PLANT ID PS#1  
 METER ID Wet Well Level  
 FIT ID n/a  
 CLIENT TAG n/a  
 OTHER n/a  
 GPS COORDINATES n/a  
 VERIFICATION DATE May 1st 2025  
 CAL. FREQUENCY Annual  
 CAL. DUE DATE May 2026

VER. BY - FM Daniel Kettlewell

Quality Management Standards Information -  
 Reference equipment and instrumentation used to  
 conduct this verification test is found in our AC-  
 QMS document at the time this test was  
 conducted.

#### PROGRAMMING PARAMETERS

EMPTY DISTANCE m 2.500  
 SPAN m 2.200  
 BLANKING DISTANCE m 0.300  
 OFFSET m 0

#### TEST CRITERIA

AS FOUND CERTIFICATION TEST Yes  
 ALLOWABLE [%] ERROR 15

#### COMPONENTS TESTED

CONVERTER DISPLAY yes  
 mA OUTPUT no  
 TOTALIZER yes  
 ACCURACY BASED ON [% o.r.] yes  
 ERROR DOCUMENTED IN THIS REPORT; BASED ON % o.r.

Ultrasonic sensor installed to ensure full scale flow condition

#### AS FOUND TEST RESULTS

		23.0					% F.S. Range
AIR SPACE MEASURED		1.993					m
<b>LEVEL EXPECTED</b>		<b>0.507</b>					m
MUT [Reading]		0.535					m
MUT [Difference]		0.028					m
MUT [% Error]		5.4					%
<b>mA OUTPUT</b>							
MUT [Reading]	min. 4.000 mA						
MUT [Difference]	max. 20.000 mA						
MUT [% Error]							

#### COMMENTS

#### QUALITY MANAGEMENT STANDARDS INFO.

[QMS] INFORMATION IDENT. ID #  
 [REFERENCE] LEVEL Sim. BOARD N/A  
 PROCESS METER PM 0

#### RESULTS

TEST	AVG % o.r.	PASS FAIL
DISPLAY	5.44	PASS
mA OUTPUT	N/A	N/A

This report reflects the test results of the overall accuracy for the above flow converter using the specified manufacturers flow tube simulator to within the specified tolerance as identified within this report.

### AS FOUND CERTIFICATION

**PASS**

#### CLIENT DETAIL

CUSTOMER OCWA – Kawartha Lakes Hub  
 CONTACT Nick Leroux  
 Senior Operations Manager  
 123 East St S  
 Bobcaygeon ON, K0M 1A0  
 P: 705-623-7278  
 E: nleroux@ocwa.com

#### EQUIPMENT DETAIL

[MUT] MANUFACTURER Miltronics  
 MODEL Multiranger 100  
 CONVERTER SERIAL NUMBER 111903138XB  
  
 PLANT ID PS#2  
 METER ID Wet Well Level  
 FIT ID n/a  
 CLIENT TAG n/a  
 OTHER n/a  
 GPS COORDINATES n/a  
  
 VERIFICATION DATE May 1st 2025  
 CAL. FREQUENCY Annual  
 CAL. DUE DATE May 2026

VER. BY - FM Daniel Kettlewell

Quality Management Standards Information -  
 Reference equipment and instrumentation used to  
 conduct this verification test is found in our AC-  
 QMS document at the time this test was  
 conducted.

#### PROGRAMMING PARAMETERS

EMPTY DISTANCE m 3.810  
 SPAN m 3.480  
 BLANKING DISTANCE m 0.300  
 OFFSET m 0

#### TEST CRITERIA

AS FOUND CERTIFICATION TEST Yes  
 ALLOWABLE [%] ERROR 15

#### COMPONENTS TESTED

CONVERTER DISPLAY yes  
 mA OUTPUT no  
 TOTALIZER yes  
 ACCURACY BASED ON [% o.r.] yes  
 ERROR DOCUMENTED IN THIS REPORT; BASED ON % o.r.

Ultrasonic sensor installed to ensure full scale flow condition

#### AS FOUND TEST RESULTS

		27.8					% F.S. Range
AIR SPACE MEASURED		2.841					m
<b>LEVEL EXPECTED</b>		<b>0.969</b>					m
MUT [Reading]		1.050					m
MUT [Difference]		0.081					m
MUT [% Error]		8.4					%
<b>mA OUTPUT</b>							
MUT [Reading]	min. 4.000 mA						
MUT [Difference]	max. 20.000 mA						
MUT [% Error]							

#### COMMENTS

#### QUALITY MANAGEMENT STANDARDS INFO.

[QMS] INFORMATION IDENT. ID #  
 [REFERENCE] LEVEL Sim. BOARD N/A  
 PROCESS METER PM 0

#### RESULTS

TEST	AVG % o.r.	PASS FAIL
DISPLAY	8.36	PASS
mA OUTPUT	N/A	N/A

This report reflects the test results of the overall accuracy for the above flow converter using the specified manufacturers flow tube simulator to within the specified tolerance as identified within this report.

### AS FOUND CERTIFICATION

**PASS**

CLIENT DETAIL		EQUIPMENT DETAIL	
CUSTOMER	OCWA – Kawartha Lakes Hub	[MUT] MANUFACTURER	Siemens
CONTACT	Nick Leroux Senior Operations Manager 123 East St S Bobcaygeon ON, K0M 1A0 P: 705-623-7278 E: nleroux@ocwa.com	MODEL	LT500
		CONVERTER SERIAL NUMBER	PBD-T1106141
		PLANT ID	PS#4
		METER ID	Wet Well Level
		FIT ID	n/a
		CLIENT TAG	n/a
		OTHER	n/a
		GPS COORDINATES	n/a
VER. BY - FM	Daniel Kettlewell	VERIFICATION DATE	May 1st 2025
Quality Management Standards Information - Reference equipment and instrumentation used to conduct this verification test is found in our AC-QMS document at the time this test was conducted.		CAL. FREQUENCY	Annual
		CAL. DUE DATE	May 2026

#### PROGRAMMING PARAMETERS

EMPTY DISTANCE	m	4.720
SPAN	m	4.720
BLANKING DISTANCE	m	0.300
OFFSET	m	0

#### TEST CRITERIA

AS FOUND CERTIFICATION TEST	Yes
ALLOWABLE [%] ERROR	15

#### COMPONENTS TESTED

CONVERTER DISPLAY	yes
mA OUTPUT	no
TOTALIZER	yes
ACCURACY BASED ON [% o.r.]	yes
ERROR DOCUMENTED IN THIS REPORT; BASED ON % o.r.	

Ultrasonic sensor installed to ensure full scale flow condition

#### AS FOUND TEST RESULTS

		37.5					% F.S. Range
AIR SPACE MEASURED		2.950					m
<b>LEVEL EXPECTED</b>		<b>1.770</b>					m
MUT [Reading]		1.800					m
MUT [Difference]		0.030					m
MUT [% Error]		1.7					%
<b>mA OUTPUT</b>							
MUT [Reading]	min. 4.000 mA						
MUT [Difference]	max. 20.000 mA						
MUT [% Error]							

#### COMMENTS

			RESULTS		
<u>QUALITY MANAGEMENT STANDARDS INFO.</u>					
[QMS] INFORMATION	IDENT.	ID #	TEST	AVG % o.r.	PASS FAIL
[REFERENCE] LEVEL	Sim. BOARD	N/A	DISPLAY	1.69	PASS
PROCESS METER	PM	0	mA OUTPUT	N/A	N/A

This report reflects the test results of the overall accuracy for the above flow converter using the specified manufacturers flow tube simulator to within the specified tolerance as identified within this report.

### AS FOUND CERTIFICATION

**PASS**

#### CLIENT DETAIL

CUSTOMER OCWA – Kawartha Lakes Hub  
 CONTACT Nick Leroux  
 Senior Operations Manager  
 123 East St S  
 Bobcaygeon ON, K0M 1A0  
 P: 705-623-7278  
 E: nleroux@ocwa.com

#### EQUIPMENT DETAIL

[MUT] MANUFACTURER Miltronics  
 MODEL Multiranger 100  
 CONVERTER SERIAL NUMBER 061004195VV  
  
 PLANT ID PS#5  
 METER ID Wet Well Level  
 FIT ID n/a  
 CLIENT TAG n/a  
 OTHER n/a  
 GPS COORDINATES n/a  
  
 VERIFICATION DATE May 1st 2025  
 CAL. FREQUENCY Annual  
 CAL. DUE DATE May 2026

VER. BY - FM Daniel Kettlewell

Quality Management Standards Information -  
 Reference equipment and instrumentation used to  
 conduct this verification test is found in our AC-  
 QMS document at the time this test was  
 conducted.

#### PROGRAMMING PARAMETERS

EMPTY DISTANCE m 3.400  
 SPAN m 3.000  
 BLANKING DISTANCE m 0.300  
 OFFSET m 0

#### TEST CRITERIA

AS FOUND CERTIFICATION TEST Yes  
 ALLOWABLE [%] ERROR 15

#### COMPONENTS TESTED

CONVERTER DISPLAY yes  
 mA OUTPUT no  
 TOTALIZER yes  
 ACCURACY BASED ON [% o.r.] yes  
 ERROR DOCUMENTED IN THIS REPORT; BASED ON % o.r.

Ultrasonic sensor installed to ensure full scale flow condition

#### AS FOUND TEST RESULTS

		42.7					% F.S. Range
AIR SPACE MEASURED		2.119					m
<b>LEVEL EXPECTED</b>		<b>1.281</b>					m
MUT [Reading]		1.300					m
MUT [Difference]		0.019					m
MUT [% Error]		1.5					%
<b>mA OUTPUT</b>							
MUT [Reading]	min. 4.000 mA						
MUT [Difference]	max. 20.000 mA						
MUT [% Error]							

#### COMMENTS

#### QUALITY MANAGEMENT STANDARDS INFO.

[QMS] INFORMATION IDENT. ID #  
 [REFERENCE] LEVEL Sim. BOARD N/A  
 PROCESS METER PM 0

#### RESULTS

TEST	AVG % o.r.	PASS FAIL
DISPLAY	1.48	PASS
mA OUTPUT	N/A	N/A

This report reflects the test results of the overall accuracy for the above flow converter using the specified manufacturers flow tube simulator to within the specified tolerance as identified within this report.

### AS FOUND CERTIFICATION

**PASS**

#### CLIENT DETAIL

CUSTOMER OCWA – Kawartha Lakes Hub  
 CONTACT Nick Leroux  
 Senior Operations Manager  
 123 East St S  
 Bobcaygeon ON, K0M 1A0  
 P: 705-623-7278  
 E: nleroux@ocwa.com

#### EQUIPMENT DETAIL

[MUT] MANUFACTURER Miltronics  
 MODEL Multiranger 100  
 CONVERTER SERIAL NUMBER PBD/W21307S5XB  
 PLANT ID PS#6  
 METER ID Wet Well Level  
 FIT ID n/a  
 CLIENT TAG n/a  
 OTHER n/a  
 GPS COORDINATES n/a  
 VERIFICATION DATE May 1st 2025  
 CAL. FREQUENCY Annual  
 CAL. DUE DATE May 2026

VER. BY - FM Daniel Kettlewell

Quality Management Standards Information -  
 Reference equipment and instrumentation used to  
 conduct this verification test is found in our AC-  
 QMS document at the time this test was  
 conducted.

#### PROGRAMMING PARAMETERS

EMPTY DISTANCE m 5.790  
 SPAN m 5.000  
 BLANKING DISTANCE m 0.300  
 OFFSET m 0

#### TEST CRITERIA

AS FOUND CERTIFICATION TEST Yes  
 ALLOWABLE [%] ERROR 15

#### COMPONENTS TESTED

CONVERTER DISPLAY yes  
 mA OUTPUT no  
 TOTALIZER yes  
 ACCURACY BASED ON [% o.r.] yes  
 ERROR DOCUMENTED IN THIS REPORT; BASED ON % o.r.

Ultrasonic sensor installed to ensure full scale flow condition

#### AS FOUND TEST RESULTS

		37.0					% F.S. Range
AIR SPACE MEASURED		3.940					m
<b>LEVEL EXPECTED</b>		<b>1.850</b>					m
MUT [Reading]		1.810					m
MUT [Difference]		-0.040					m
MUT [% Error]		-2.2					%
<b>mA OUTPUT</b>							
MUT [Reading]	min. 4.000 mA						
MUT [Difference]	max. 20.000 mA						
MUT [% Error]							

#### COMMENTS

#### QUALITY MANAGEMENT STANDARDS INFO.

[QMS] INFORMATION IDENT. ID #  
 [REFERENCE] LEVEL Sim. BOARD N/A  
 PROCESS METER PM 0

#### RESULTS

TEST	AVG % o.r.	PASS FAIL
DISPLAY	-2.16	PASS
mA OUTPUT	N/A	N/A

This report reflects the test results of the overall accuracy for the above flow converter using the specified manufacturers flow tube simulator to within the specified tolerance as identified within this report.

### AS FOUND CERTIFICATION

**PASS**

#### CLIENT DETAIL

CUSTOMER OCWA – Kawartha Lakes Hub  
 CONTACT Nick Leroux  
 Senior Operations Manager  
 123 East St S  
 Bobcaygeon ON, K0M 1A0  
 P: 705-623-7278  
 E: nleroux@ocwa.com

#### EQUIPMENT DETAIL

[MUT] MANUFACTURER Siemens  
 MODEL LT500  
 CONVERTER SERIAL NUMBER N/A  
  
 PLANT ID PS#7  
 METER ID Wet Well Level  
 FIT ID n/a  
 CLIENT TAG n/a  
 OTHER n/a  
 GPS COORDINATES n/a  
  
 VERIFICATION DATE May 1st 2025  
 CAL. FREQUENCY Annual  
 CAL. DUE DATE May 2026

VER. BY - FM Daniel Kettlewell

Quality Management Standards Information -  
 Reference equipment and instrumentation used to  
 conduct this verification test is found in our AC-  
 QMS document at the time this test was  
 conducted.

#### PROGRAMMING PARAMETERS

EMPTY DISTANCE m 5.855  
 SPAN m 1.000  
 BLANKING DISTANCE m 0.300  
 OFFSET m 0

#### TEST CRITERIA

AS FOUND CERTIFICATION TEST Yes  
 ALLOWABLE [%] ERROR 15

#### COMPONENTS TESTED

CONVERTER DISPLAY yes  
 mA OUTPUT no  
 TOTALIZER yes  
 ACCURACY BASED ON [% o.r.] yes  
 ERROR DOCUMENTED IN THIS REPORT; BASED ON % o.r.

Ultrasonic sensor installed to ensure full scale flow condition

#### AS FOUND TEST RESULTS

		101.0					% F.S. Range
AIR SPACE MEASURED		4.845					m
<b>LEVEL EXPECTED</b>		<b>1.010</b>					m
MUT [Reading]		1.060					m
MUT [Difference]		0.050					m
MUT [% Error]		5.0					%
<b>mA OUTPUT</b>							
MUT [Reading]	min. 4.000 mA						
MUT [Difference]	max. 20.000 mA						
MUT [% Error]							

#### COMMENTS

#### QUALITY MANAGEMENT STANDARDS INFO.

[QMS] INFORMATION IDENT. ID #  
 [REFERENCE] LEVEL Sim. BOARD N/A  
 PROCESS METER PM 0

#### RESULTS

TEST	AVG % o.r.	PASS FAIL
DISPLAY	4.95	PASS
mA OUTPUT	N/A	N/A

This report reflects the test results of the overall accuracy for the above flow converter using the specified manufacturers flow tube simulator to within the specified tolerance as identified within this report.

### AS FOUND CERTIFICATION

**PASS**

#### CLIENT DETAIL

CUSTOMER OCWA – Kawartha Lakes Hub  
 CONTACT Nick Leroux  
 Senior Operations Manager  
 123 East St S  
 Bobcaygeon ON, K0M 1A0  
 P: 705-623-7278  
 E: nleroux@ocwa.com

#### EQUIPMENT DETAIL

[MUT] MANUFACTURER Siemens  
 MODEL LT500  
 CONVERTER SERIAL NUMBER PBD-T40473017  
 PLANT ID PS#8  
 METER ID Wet Well Level  
 FIT ID n/a  
 CLIENT TAG n/a  
 OTHER n/a  
 GPS COORDINATES n/a  
 VERIFICATION DATE May 1st 2025  
 CAL. FREQUENCY Annual  
 CAL. DUE DATE May 2026

VER. BY - FM Daniel Kettlewell

Quality Management Standards Information -  
 Reference equipment and instrumentation used to  
 conduct this verification test is found in our AC-  
 QMS document at the time this test was  
 conducted.

#### PROGRAMMING PARAMETERS

EMPTY DISTANCE m 7.000  
 SPAN m 6.700  
 BLANKING DISTANCE m 0.300  
 OFFSET m 0

#### TEST CRITERIA

AS FOUND CERTIFICATION TEST Yes  
 ALLOWABLE [%] ERROR 15

#### COMPONENTS TESTED

CONVERTER DISPLAY yes  
 mA OUTPUT no  
 TOTALIZER yes  
 ACCURACY BASED ON [% o.r.] yes  
 ERROR DOCUMENTED IN THIS REPORT; BASED ON % o.r.

Ultrasonic sensor installed to ensure full scale flow condition

#### AS FOUND TEST RESULTS

		27.2					% F.S. Range
AIR SPACE MEASURED		5.176					m
<b>LEVEL EXPECTED</b>		<b>1.824</b>					m
MUT [Reading]		1.820					m
MUT [Difference]		-0.004					m
MUT [% Error]		-0.2					%
<b>mA OUTPUT</b>							
MUT [Reading]	min. 4.000 mA						
MUT [Difference]	max. 20.000 mA						
MUT [% Error]							

#### COMMENTS

#### QUALITY MANAGEMENT STANDARDS INFO.

[QMS] INFORMATION IDENT. ID #  
 [REFERENCE] LEVEL Sim. BOARD N/A  
 PROCESS METER PM 0


#### RESULTS

TEST	AVG % o.r.	PASS FAIL
DISPLAY	-0.22	PASS
mA OUTPUT	N/A	N/A

This report reflects the test results of the overall accuracy for the above flow converter using the specified manufacturers flow tube simulator to within the specified tolerance as identified within this report.

# APPENDIX III

Biosolids Summary



Biosolids Quality Report

Facility: LAGOON CITY WASTEWATER TREATMENT PLANT



Solids & Nutrients

Period: 01/01/2025 to 12/31/2025

Works: 1617 / Digester Type: Aerobic

Solids & Nutrients	Metals & Criteria	Last 4 Samples
--------------------	-------------------	----------------

Facility Works Number: 120002255 Receiver: Wetland area draining to Lake Simcoe  
 Facility Owner: Municipality: The Township of Ramara Service Population: 2420  
 Facility Classification: Class 2 Wastewater Treatment Total Design Capacity:

Note: all parameters in this report are derived from the Bslq Station

Month	Hauled Vol. (m³)	Total Solids (mg/L)	Volatile Solids (mg/L)	Total Phosphorus (mg/L)	Total Ammonia Nitrogen (mg/L)	Nitrate as N (mg/L)	Nitrite as N (mg/L)	Total Kjeldahl Nitrogen (mg/L)	Ammonia + Nitrate (mg/L)	Potassium (mg/L)
Parameter Short Name	HauledVol	TS	VS	TP	NH3p_NH4p_N	NO3-N	NO2-N	TKN	Calculation in Report	K
T/S	IH Month.Total	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	- no T/S	Lab Published Month Mean
Jan		17,300.00	8,490.00	410.00	2.50	3.00	3.00	518.00	2.75	41.00
Feb		17,000.00	8,800.00	353.00	1.70	3.00	3.00	501.00	2.35	39.70
Mar		17,900.00	9,120.00	312.00	2.30	3.00	3.00	523.00	2.65	85.00
Apr		30,100.00	14,900.00	274.00	2.40	3.00	3.00	825.00	2.70	30.00
May	816.00	28,000.00	13,400.00	549.00	1.90	3.00	3.00	678.00	2.45	46.00
Jun		31,400.00	15,500.00	586.00	4.40	3.00	3.00	526.00	3.70	60.00
Jul		29,200.00	13,500.00	620.00	3.40	3.00	3.00	396.00	3.20	60.00
Aug		36,100.00	16,800.00	848.00	5.10	40.00	3.00	932.00	22.55	69.00
Sep		42,100.00	19,700.00	857.00	5.40	3.00	3.00	918.00	4.20	66.00
Oct	456.00	39,600.00	18,900.00	1,070.00	13.80	21.00	3.00	770.00	17.40	74.00
Nov	160.00	29,500.00	14,600.00	732.00	1.00	16.00	3.00	637.00	8.50	60.00
Dec		26,100.00	12,200.00	568.00	1.30	3.00	3.00	791.00	2.15	59.00
<b>Average</b>	477.33	28,691.67	13,825.83	598.25	3.77	8.67	3.00	667.92	6.22	57.48
<b>Total</b>	1,432.00	344,300.00	165,910.00	7,179.00	45.20	104.00	36.00	8,015.00	74.60	689.70

Solids & Nutrients

**Metals & Criteria**

Last 4 Samples

Note: all parameters in this report are derived from the Bslq Station

Month	Arsenic (mg/L)	Cadmium (mg/L)	Cobalt (mg/L)	Chromium (mg/L)	Copper (mg/L)	Mercury (mg/L)	Molybdenum (mg/L)	Nickel (mg/L)	Lead (mg/L)	Selenium (mg/L)	Zinc (mg/L)
Parameter Short Name	As	Cd	Co	Cr	Cu	Hg	Mo	Ni	Pb	Se	Zn
T/S	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean	Lab Published Month Mean
Jan	0.10	0.01	0.04	0.34	2.80	0.01	0.05	0.20	0.20	0.10	7.00
Feb	0.11	0.01	0.04	0.30	2.38	0.01	0.05	0.18	0.14	0.10	6.48
Mar	0.10	0.06	0.10	0.71	28.00	0.03	0.33	0.61	0.90	0.10	46.00
Apr	0.10	0.01	0.03	0.21	1.90	0.01	0.05	0.13	0.10	0.10	5.00
May	0.20	0.01	0.05	0.42	3.70	0.01	0.05	0.25	0.20	0.10	9.00
Jun	0.20	0.01	0.07	0.47	3.50	0.01	0.05	0.32	0.20	0.10	9.00
Jul	0.20	0.01	0.06	0.40	3.60	0.01	0.05	0.31	0.20	0.10	9.00
Aug	0.20	0.02	0.08	0.56	5.80	0.02	0.07	0.43	0.30	0.10	15.00
Sep	0.20	0.02	0.09	0.62	6.50	0.01	0.07	0.46	0.30	0.10	15.00
Oct	0.30	0.03	0.09	0.70	7.40	0.02	0.09	0.53	0.40	0.10	18.00
Nov	0.20	0.02	0.06	0.53	5.70	0.01	0.06	0.38	0.30	0.10	13.00
Dec	0.10	0.01	0.06	0.42	4.30	0.01	0.05	0.31	0.20	0.10	10.00
Average	0.17	0.02	0.06	0.47	6.30	0.01	0.08	0.34	0.29	0.10	13.54
Max. Permissible Metal Concentrations (mg/kg of Solids)	170.00	34.00	340.00	2,800.00	1,700.00	11.00	94.00	420.00	1,100.00	34.00	4,200.00
Metal Concentrations in Sludge (mg/kg)	5.82	0.65	2.23	16.50	219.52	0.35	2.82	11.93	10.00	3.49	471.91

Solids & Nutrients

Metals & Criteria

**Last 4 Samples**

Note: all parameters in this report are derived from the Bslq Station

Parameter Short Name	Time Series	09/04/2025	10/07/2025	11/03/2025	12/02/2025	Average	Metal Concentrations in Sludge (mg/kg)	Max. Permissible Metal Concentrations (mg/kg of Solids)
As (mg/L)	Lab Published	0.20	0.30	0.20	0.10	0.20	5.83	170
Cd (mg/L)	Lab Published	0.02	0.03	0.02	0.01	0.02	0.58	34
Co (mg/L)	Lab Published	0.09	0.09	0.06	0.06	0.08	2.18	340
Cr (mg/L)	Lab Published	0.62	0.70	0.53	0.42	0.57	16.53	2800
Cu (mg/L)	Lab Published	6.50	7.40	5.70	4.30	5.98	174.07	1700
Hg (mg/L)	Lab Published	0.01	0.02	0.01	0.01	0.01	0.31	11
Mo (mg/L)	Lab Published	0.07	0.09	0.06	0.05	0.07	1.97	94
Ni (mg/L)	Lab Published	0.46	0.53	0.38	0.31	0.42	12.24	420
Pb (mg/L)	Lab Published	0.30	0.40	0.30	0.20	0.30	8.74	1100
Se (mg/L)	Lab Published	0.10	0.10	0.10	0.10	0.10	2.91	34
Zn (mg/L)	Lab Published	15.00	18.00	13.00	10.00	14.00	407.87	4200
E.Coli Dry Wt (cfu/g)	Lab Published						E. Coli average is the GMD	
TS (mg/L)	Lab Published	42,100.00	39,600.00	29,500.00	26,100.00	34,325.00		
VS (mg/L)	Lab Published	19,700.00	18,900.00	14,600.00	12,200.00	16,350.00		
TP (mg/L)	Lab Published	857.00	1,070.00	732.00	568.00	806.75		
NO2-N (mg/L)	Lab Published	3.00	3.00	3.00	3.00	3.00		
TKN (mg/L)	Lab Published	918.00	770.00	637.00	791.00	779.00		
K (mg/L)	Lab Published	66.00	74.00	60.00	59.00	64.75		
NH3p_NH4p_N (mg/L)	Lab Published	5.40	13.80	1.00	1.30	5.38		
NO3-N (mg/L)	Lab Published	3.00	21.00	16.00	3.00	10.75		

# APPENDIX VI

Weekly Effluent Parameter Reports



**Customized Daily Vertical Report**

From 01/01/2025 to 12/31/2025

Facility Name: LAGOON CITY WASTEWATER TREATMENT PLANT  
Receiver: Wetland area draining to Lake Simcoe

Facility Org Number: 1617  
Facility Owner: Municipality: The Township of Ramara  
Service Population: 2420

Works: 120002255  
Facility Classification: Class 2 Wastewater Treatment  
Total Design Capacity:



Final Effluent						
	Carbonaceous Biochemical Oxygen Demand: CBOD5 - mg/L		Total Phosphorus: TP - mg/L	Total Suspended Solids: TSS - mg/L		
	Lab		Lab	Lab		
01/06/2025		5.00	0.04		5.00	
01/13/2025	<	4.00	0.05		3.00	
01/20/2025	<	4.00	0.03	<	2.00	
01/27/2025	<	4.00	0.15		11.00	
Total	<	17.00	0.27	<	21.00	
Avg	<	4.25	0.07	<	5.25	
Max		5.00	0.15		11.00	
Min	<	4.00	0.03	<	2.00	
02/03/2025	<	4.00	0.04		2.00	
02/11/2025	<	4.00	0.04		2.00	
02/18/2025		5.00	0.06	<	2.00	
02/24/2025	<	4.00	0.06	<	2.00	
Total	<	17.00	0.20	<	8.00	
Avg	<	4.25	0.05	<	2.00	
Max		5.00	0.06		2.00	
Min	<	4.00	0.04	<	2.00	
03/03/2025	<	4.00	0.06		4.00	
03/10/2025	<	4.00	0.04	<	2.00	
03/18/2025		4.00	1.33		108.00	
03/24/2025	<	4.00	0.03		2.00	
Total	<	16.00	1.46	<	116.00	
Avg	<	4.00	0.37	<	29.00	
Max		4.00	1.33		108.00	
Min	<	4.00	0.03	<	2.00	
04/02/2025	<	4.00	<	0.03	<	2.00
04/06/2025	<	4.00	<	0.03		4.00
04/14/2025	<	4.00	<	0.03	<	2.00
04/22/2025	<	4.00	<	0.03	<	2.00
04/28/2025	<	4.00	<	0.03		2.00
Total	<	20.00	<	0.15	<	12.00
Avg	<	4.00	<	0.03	<	2.40
Max	<	4.00	<	0.03		4.00
Min	<	4.00	<	0.03	<	2.00
05/05/2025	<	4.00		0.04		3.00

-1 :  
More than one value reported/day  
Extracted: 4/8/2026 11:27:00 AM

Total Execution: 3.32 seconds  
User: OCWA\lamiotna, URL: /Customized Reports

**Customized Daily Vertical Report**

From 01/01/2025 to 12/31/2025

Facility Name: LAGOON CITY WASTEWATER TREATMENT PLANT  
Receiver: Wetland area draining to Lake Simcoe

Facility Org Number: 1617  
Facility Owner: Municipality: The Township of Ramara  
Service Population: 2420

Works: 120002255  
Facility Classification: Class 2 Wastewater Treatment  
Total Design Capacity:



05/12/2025	<	4.00		0.03		2.00
05/20/2025	<	4.00		0.04		3.00
05/26/2025	<	4.00		0.04		3.00
Total	<	16.00		0.15		11.00
Avg	<	4.00		0.04		2.75
Max	<	4.00		0.04		3.00
Min	<	4.00		0.03		2.00
06/02/2025	<	4.00	<	0.03		2.00
06/09/2025	<	4.00		0.04		3.00
06/16/2025	<	4.00	<	0.03		3.00
06/23/2025	<	4.00		0.03	<	2.00
06/30/2025	<	4.00		0.05	<	2.00
Total	<	20.00	<	0.18	<	12.00
Avg	<	4.00	<	0.04	<	2.40
Max	<	4.00		0.05		3.00
Min	<	4.00	<	0.03	<	2.00
07/07/2025	<	4.00		0.04		2.00
07/14/2025	<	4.00	<	0.03	<	2.00
07/21/2025	<	4.00		0.05	<	2.00
07/28/2025	<	4.00		0.05		2.00
Total	<	16.00	<	0.17	<	8.00
Avg	<	4.00	<	0.04	<	2.00
Max	<	4.00		0.05		2.00
Min	<	4.00	<	0.03	<	2.00
08/05/2025	<	4.00		0.04	<	2.00
08/11/2025	<	4.00		0.04	<	2.00
08/18/2025	<	4.00		0.04	<	2.00
08/25/2025	<	4.00	<	0.03		2.00
Total	<	16.00	<	0.15	<	8.00
Avg	<	4.00	<	0.04	<	2.00
Max	<	4.00		0.04		2.00
Min	<	4.00	<	0.03	<	2.00
09/02/2025	<	4.00		0.06		3.00
09/08/2025	<	4.00		0.04		2.00
09/15/2025	<	4.00		0.05	<	2.00
09/22/2025	<	4.00		0.03		2.00
09/29/2025	<	4.00		0.04		2.00
Total	<	20.00		0.22	<	11.00
Avg	<	4.00		0.04	<	2.20
Max	<	4.00		0.06		3.00
Min	<	4.00		0.03	<	2.00

-1 :

More than one value reported/day

Extracted: 4/8/2026 11:27:00 AM

Total Execution: 3.32 seconds

User: OCWA\lamiotna, URL: /Customized Reports

**Customized Daily Vertical Report**

From 01/01/2025 to 12/31/2025

Facility Name: LAGOON CITY WASTEWATER  
TREATMENT PLANT  
Receiver: Wetland area draining to Lake Simcoe

Facility Org Number: 1617  
Facility Owner: Municipality: The Township of Ramara  
Service Population: 2420

Works: 120002255  
Facility Classification: Class 2 Wastewater Treatment  
Total Design Capacity:



10/06/2025	<	4.00	<	0.03	<	2.00
10/14/2025	<	4.00	<	0.03	<	2.00
10/20/2025	<	4.00	<	0.03	<	2.00
10/27/2025	<	4.00	<	0.03	<	2.00
Total	<	16.00	<	0.12	<	8.00
Avg	<	4.00	<	0.03	<	2.00
Max	<	4.00	<	0.03	<	2.00
Min	<	4.00	<	0.03	<	2.00
11/03/2025	<	4.00		0.04	<	2.00
11/10/2025	<	4.00	<	0.03		2.00
11/17/2025	<	4.00	<	0.03		2.00
11/24/2025	<	4.00	<	0.03	<	2.00
Total	<	16.00	<	0.13	<	8.00
Avg	<	4.00	<	0.03	<	2.00
Max	<	4.00		0.04		2.00
Min	<	4.00	<	0.03	<	2.00
12/01/2025	<	4.00	<	0.03	<	2.00
12/08/2025	<	4.00	<	0.03	<	2.00
12/15/2025	<	4.00	<	0.03		2.00
12/22/2025	<	4.00		0.04		3.00
12/29/2025	<	4.00	<	0.03		3.00
Total	<	20.00	<	0.16	<	12.00
Avg	<	4.00	<	0.03	<	2.40
Max	<	4.00		0.04		3.00
Min	<	4.00	<	0.03	<	2.00
